WTCI-337-P

# WALTER SCHLEIF
# GOLD LOGBOOK

PX-751

First Aid Rm 51 Dey Street
"Ext 51 - when closed
call SU-2-1290

Beekman Hosp BE-3-5300

W. SCHLEIF

400 Curtain Wall
Column Covers

110 Carpentry. Dry wall
A-AB 213
Install Doors. A-AB-213-A

113 Spraying Cafes on Trusses

107 Resilient Tile floors

106 Marble

109 Wall & Floor Tile

Burt Weinstein 11 floor sect
964-8691

Mario De Bona 732-5222

Star Circle 349-7380

3-31 9-30
4 31
5 31
6-31
7 31
8 31 3-31-70 STEWART

At Personnel -
At Job Site 11 AM - sent to 2nd
floor to await Ed
told to go with Jim
to get aquaintance with Job

4-1-70
Same as above.
Application of Epoxy to adhere Asbestos
to columns.

4-2-70
to Personnel to have Prints &
Photos & Issuance of ID Card to
Job Site 10 AM -
the application of Epoxy & the
coating of Asbestos is questionable
I believe that everyone is trying
to hang their hat on any thing they
they possibly can to come up with
a solution to this problem.

4-8-70




X = metal above Roof
Problem setting Hoop

On East & West Stair Forms have Bumper Holes - Center Stair has none - Specs Call for all - What is deviation? -

4-8-70
Gauge made out of Tubing 3" under to check Haunch Forms. #1 & 2
Gauge 3/16 under for Center #3

| | EAST | Center | WEST |
|---|---|---|---|
| 18 | 1/8 - | ok | ok |
| 17 | 1/8 - | ok | ok |
| 16 | ok | ok | 1/8 - |
| 15 | ok | ok | ok |
| 14 | 1/8 - | ok | ok |
| 13 | ok | ok | 1/8 - |
| 12 | ok | ok | 1/8 - |
| 11 | 1/16 - | NG 3/16 - | 1/8 - |
| 10 | 1/8 - | ok | NG |

Sheet Rock Problem - Distance between BB in Forms = 3 7/8 -

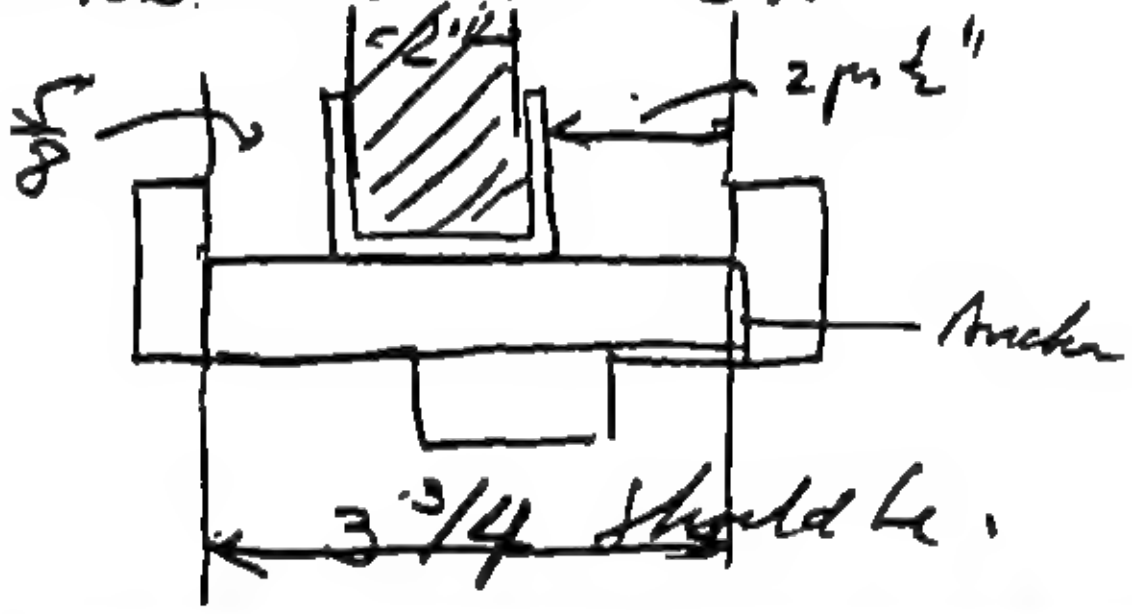

4-9-

16 floor SE Elevator Shaft
first layer of Shaft Rock some
panels are not Contact to concrete
app 2" short top - Bottom they
are filling in Voids with Pcs -

NE Elev Shaft Corridor poor
workmanship on Core Board
They are cutting both Core Board
& channels to some length
and shimming up Bottom
to Hang on to top this is also being
done at other Site
18th floor N W Shaft Hoisting
cables in concrete -- Star Circle
are notching 1" Runner and they
will have to notch Core board
to pass cables -
Bolts on Elev Header to Struts
are running into corridor thereby
Star Circle have to cut the Core
Board to fit if bolts were Elevator
removed into shaft this could be

4-10

Spoke to Tom - Star Circle Re Shim bott
of Core Boards - He instructed his
men to conform to specs -

Fair

4-11 Sat

SW-12 - Painter 12
Iron Workers 5
Col Cover Corp 38+

Note: 11 Col Covers EPONOL Did not dry - even overnight. They are going to strip with MEK & Re...

NE-12 Painter 9
Iron Workers 5
Col Cover Corp 55
Spraying Cafco on Columns - EAST

NE 14 Painter - 11 + 1 foreman
Iron Workers - 4
Col Cover Corp - 60
Spraying Cafco on Columns EAST - South

Painters total (32 + 1 foreman)
Iron Workers 14 } Col Covers
4 Caulking CC

15 floor Setting up for Monday

1 floor 19 Covers Epanol did not Dry Starting

4-11

34th fl Barricade down on North End of Elevators 6-7 - by Ulmer

Temp Bars put across front

41st fl 2 men spraying Cafco on Beams & Trusses

55th fl 2 men spraying Trusses

3 men Hanging Tarps

9th fl NW - 4 Iron Workers Cleaning out Caulking Col Covers. Patching Cafco on N Side

10th fl - MEK Test in Safety Cans?

DeBrino total 400
1 Supt
2 Foremen
13 Mech
2 Engineers
23 Labor

113
1 Foreman
4 Mech
12 Labor

4 PM

4-13-70 FAIR 110

See 4-8

110

4-14-70 FAIR

TUESDAY

20th floor West Stairwell.

Brick cut for 1/2" ~~[illegible]~~ on Stairwell & 1" on Corridor - They must use 1/2" SR on Stairwell instead of SR & 2 pcs 1/2" SR on corridor - Single being set now.

4-15-70 Office

West Stair
20 fl Mock up of Door Frame using 1/2" Sheet Rock Stair Side & 2 pcs 1/2" Sheet Rock Corridor Side - Tight fit.

4-16-70 -

Sam of Star Circle stated that he cannot wait for extra Test... on his office he is going ahead & setting Bucks as samples 20 fl. W. Spoke to Lucarelli & Sam. They should contact the proper parties to see about changes - then above

Cove Board. Elect Closet 35 fl.
Back to check 23 floor STL
Spraying Cafco on Truss 41 fl.
Rodding Taps 37 fl.
Spraying Cafco on Truss 36 fl
Rodding Taps 35 floor

4-17-70 Fair

Protection on El Shafts - does this pertain to every floor or every other floor?? & if every other floor should it be Planked Complete

---

4-19-70 #1817

1 Foreman
1 Steward 8-5:30
7 Cpt -
Sunday

4-20-70 Rain

Safety with Fred Stuyvesant - to Die Underdecks - Spoke to Sid Philips Contract Supr at office - 47th floor - 3 shafts open 38-39-40 - We are to speak to Don De Paulo Die Mick Foreman - Tinker Cindy Barbara

24 floor Wire Raceway into corridor Rock-lath not going in true - They also Remove 1" of Rock 30 Shaft Spoke to Warren Market Tinker

Stair West 17-18 19 out - Spoke to

Shafts 7-8-9 floors 12-13-14-15-17-19 Removed for saddles - no saddles Called for - Die to fill - Warren told

Shaft 20-21 Concrete forms - 17 fl not removed - Warren told.

4-21-70 ~~Fair~~ Cloudy

DiBona Taps taking down on 41
Taps going up on 39
Taps up on 38-
37 fl Taps up 50% Comp on Trusses
Wait Spraying - Stop - 3 men cleaning floor.
Hanging Taps outside N-S-W Elev 26 floor.

Star Circle Started Setting Frames in Elect Closets 36 fl N 33 fl N. using Buck #AER1 holding ½" inside & 2 pcs 1/2" outside wait 2" Core Should be 5/8 Inside See Shop #59 FCA details
Star Circle missed few clips When shooting in "J" Channel 21 fl NE Shaft - 20 fl North West Shaft 17 fl opp Center Stair

4-22-70 Fair

AER

37 NE Elect Room · Sides No Buck
36 Wait Buck
35 " "
34 No Buck
33 Wait "
32 Wait "
31 S & H Set only
31 SW S-H Set only
26 NE Sides No Buck
25 " " " "
24 } none
23 }
22 NE Sides No Buck
23 Setting Stair Well Bucks - Also set 22-21-20-19-18-17-16-15-14-13-12-11

AJR

Telephone Rooms started 3 Sides No Front Walls or Door Frames can be Set - There is no Steel Stud Part on Job.

4-23-70 Lea Rain

1PM

Spoke to Fred Corrado (Tishman) Re 41 fl that De Bonn sprayed bottom of Beams that the Steamfitters are complaining that in their removal the Cafco is going down their Backs & they itch severely after they take a Bath. Fred was surprised that they take Baths. He is going to contact De Bonn to Respond. at 4 PM checked with Fred & he could not get in touch with De Bonn. Will Try tomorrow AM.

Notified by Tom of Star Circle that They are working Saturday 4-25-70 on Shaft #39-40-41 with Core Board & Rock where required. from 40 then 3 Crews 1 at middle 1 at Bottom Will work till they complete

4-24-70 Cloudy Rainy

Spoke again to Fred Corrado he was still unable to get an answer from De Bonn Regarding Spray Beams 41 fl.

Contacted by Star Circle Re Sat Work. 4-25 They Will Start on 40 fl Shaft # 39-40-41 & complete Core & Sheet Rock. a Crew of 40 Men are anticipated

Spoke to Star Re short Core Board. No Shims Will be tolerated -

4-25- Fair
Sat

Star Circle working on Shafts #39-40-41 from 39 down to 18 Installing J & H channels Installing Core Board & Sheet Rock 1 Supt. 1 Asst Supt 3 Foremen - 1 Shop Steward - 1 Coffee Boy 38 Men total 45 men Sat.

On 39 fl. Shaft #40 Frank VAGNINI while using Star Stud Driver on J channel on floor slipped and shot through his left palm. Man was taken to Hospital by Port Doctor & Blackie of Star Accident occurred at 10:20 AM

Trusses sprayed above 28
28-29-30-31-32-33-34-35-36
50% Comp - 37-41
Tarps up ready to spray 38-39
No Tarps on 40.

4-27- Fair
Mon

Inspected Core Board Installation found many places where fire stop & adjacent walls not tied together - Spoke to Sean - he asked me to mark spots with Ⓢ & he would send some one to correct same there are locations where Core Board is short

4-28 - Fair

Marking all location on Core Board from 10 to 38 Inc where Tie in screws were left out Star Circle is following up and inserting same

Questioned location of Elevator Frames in relationship to Core Board - Letter from B. Wernstein to Star Circle to hold 2 1/2" between edge of Buck to Core Board to enable sufficient Room for Marble - Letter Dated April 28.

Met With Joe Iaccarelli of Star re payment he made appointment to meet With Mr on Thursday 1 PM

Sirdon shipped Material today from # ATR-1 - AWTR-1 - AU401 AC005-1 - plus 43 Sills for Tele & Electric Closet - (Sam)

4-29 Fair

38 floor Shaft 42 Corridor "H" Section Left out between 2 pcs Core Board for Removable at later date

Otis is resetting Bucks on 15 floor Shaft 29-28-27 & setting doors they are shimming Buck & plumbing & racking and screwing into Core Board & "C" Channel Note: No sheet Rock has been put on there as yet

Shaft #5 Will be Screened in from Lobby to 39 same ~~Shafts on~~ floors will have Core Board when possible

Dr Bona recieved new Material Cafco today - started spraying Columns Will start to spray Trusses when he receives more material -

4-30 Clourly

N = NO
P = Partial
C = Comp

| Fl | Core Board (on floor) | Heat Coil | Layout | Stair Broth | J Elec only | NE Elect NO Board | Tel | H/A SW |
|---|---|---|---|---|---|---|---|---|
| 40 | N | N | P | N | | P | N | N |
| 39 | Y | Y | Y | N | 0%40 | P | N | |
| 38 | Y | Y | P | N | N | N | N | |
| 37 | Y | Y | P | N | 0%40 | P | N | |
| 36 | Y | Y | Y | N | 0%40 | C | N | |
| 35 | Y | Y | Y | N | 0%0 | C | N | |
| 34 | Y | Y | Y | N | 0%0 | C | N | |
| 33 | Y | Y | Y | N | 0%0 | C | N | |
| 32 | Y | Y | Y | N | 0%0 | C | N | |
| 31 | Y | Y | Y | N | 0%40 | C | N | |
| 30 | Y | Y | Y | N | N | N | N | |
| 29 | Y | Y | Y | N | N | N | N | |
| 28 | Y | Y | Y | N | N | N | N | |
| 27 | Y | Y | Y | N | N | N | N | [illegible] |
| 26 | Y | Y | Y | Y | S | Y | N | P |
| 25 | Y | Y | Y | Y | S | Y | N | N |
| 24 | Y | Y | Y | Y | P | N | N | N |
| 23 | Y | Y | Y | Y | P | N | N | P |
| 22 | Y | Y | Y | Y | P | N | N | P |
| 21 | Y | Y | Y | Y | P | N | N | P |
| 20 | | | | | | | | |

5-1- Fair

Otis men letting Bucks Plumb & posting to Core Board using shims and straps where required Then Hanging down -

Has Running Protection both Hoisting & Core Board

Saddles being grouted 25 down

5-4-70 - Cloudy 50°

[illegible] [illegible] Glen Circle
Westman [illegible] Completion
then checked out with
Boris & [illegible]
Tower A & B -

5-5-70 - fair — 50°

Checked All Open [illegible] in
Spandrels at Hinge Joint 40 &
Roof - (101) pcs.

DeBona starting [illegible] [illegible]
on 37 floor. ~~NW Elevator~~
& closing floor [illegible] [illegible]
38 fl -

| CONTRACT NO. | CONTRACTOR | WEATHER |
|---|---|---|
| 113 | D. Bone | Fair |

Status of floors

| | |
|---|---|
| 41 fl Trusses only No Core col | 25% |
| 38 " " " " | 15% |
| 37 " " " " | 25% |
| 31 to 30 Inc " " " | 50% |
| 29 to 9 Inc Truss & Core Col | 70% |
| 8 Core Col only Truss not done | 20% |
| 7 fl Core Col only - No Truss on floor | 80% |
| 6 fl Core Col only Truss not Done | 20% |

[illegible] INSPECTOR 5-6-70 DATE Day SHIFT REVIEWED BY

INSPECTOR'S DAILY NARRATIVE

| CONTRACT NO. | CONTRACTOR | WEATHER |
|---|---|---|
| 113 | D. Bone | Fair |

5 to 2 Inc. Core only - No Truss on floor 80%

Note - I have given 65% for Trusses & 35% for core col and have deducted from Truss %. 5% for PT Cell, 5% for Damaging unit Connection & 5% for Voids & Holddown on Core Col deduct % 7 5% for Voids & Holddown & 10% for insufficient [illegible]

[illegible] INSPECTOR 5-6-70 DATE Day SHIFT REVIEWED BY

Fair
Cool

~~Top Plate Bay Pl~~ 5 floors / wk

Core Board 3 floors / wk

Layout 5 floors / wk

Bonis 40 -

See Special Report dated 5-7-70 on De Bona - Fred Corrado - Bert Vicente Re 41 fl - Bott of Beams Scraping for Sand Counter

---

5-7-70 - Fair

(110)

21 fl 2 Men Inst Plank
22 fl 12 Men Inst Plank & Shot
23 6 Men Inst Plank & Shot
22-23 3 Men Pick up forming
22-23 3 Men Protection
25 2 Men Framing Machine Room
24 2 Men Inst Studs
26-27 28-29 2 Men Bott & Top Track Stairs
31 5 Men Top Track
30 1 Man Bott Track
16-17-18-23 - 4 Men Inst Plank El Shaft #5 Bott Lug
26 2 Men Layout Mach Room
22 to 34 6 Men Protection
2 Men Coffee & Pick up Material
2 Men Labor
3 Foremen
1 Asst Super
1 Super

58 Men

Bucks Rec FDC
AS044
AS042
AS045
AS043

4:30 Sat to 12 mid

6 7 Shaft

1 Hoist Elev 10 to 34 All day Sunday

May 8-70 - Fair

23 14 men Inst Plank & Sheet
22 4 men Inst "
22-23 2 men Pick up forming
22-23 4 men Protection
32 fl 2 men Plumb for Top Track
32 - 4 men Inst Top Track
31 1 man bottom Tracks
" (2) men Setting Bucks
" (2) men forming Stairs
25 2 men Forming Top & Bot Track Motor Room
25 4 men Cutting Studs
6 fl 2 men Layout
37 2 men Layout
2 Labor
4 men Removing Protection
2 men Coffee & Pick up Inst
21-22-23 2 men Install Bucks, Plank North-South Elect Closet
3 Foremen
58 men 1 Asst Supt
1 Supt

May 9-70 Sat Fair
3:30/12:30

Star Circle Stripped Protection Shaft #6-7 - on South E East Wall Installed Scaffolds - Top - Bott Track - H Section & Completed 4 floors with Core Board & Sheet Rock for 10 to 32 Inc

(35)

30
1 Lab
4 Sup.

(35)

5 10-70 Sun.
Fair

25 floors done
10 to 34 Inc

Rem Peat
Layout
T-B Track
H
Core
Sheet Rock
Rem Plank
Close up

Average
18 Men
Average/Floor

26 Men
4 Fore

4 Men Worked to 10 PM — 1 Welder
Sunday Cleaning — 1 dS
Shaft & top of Cab — 32 Men

5-11-70 Mon
Fair

78 Sheet Rock Del & Dist
on floors 9 to 16 Inc.

113-Contract as per Jimmy Blue
Eyes- No Work on this today.

Otis claims they will join
car #5 to start to construct
Temp Enclosure Tuesday 5-12-70
It will take them two days to
construct this cab-

Shaft #6- East Wall been off
Channel Welded to Column
24 Plank & Sheet
23 Plank & Sheet
23-24 Protection 10 & 34
33 Top Track
32 Frame Stairs & Backs- Bath Track
25 Framing Mach Room
26 Duct Heads
6-5-37 Layout
23-24- Plank East Clos H E S-

60 Men

5-12-70 Fair
Tuesday

113 - Started 1 PM on keeping Bolt flanges of Beams on 41 ft North Side over shaft.

Plumbers scaffold being set up South East 41 ft

44 - Layout - 45
45-46-44-47 Cutting studs
33 Plumbing Top track & Top track
24-27 - Framing shaft - 48-35-37-38
26 - Inst studs
23-24 - Plank & sheet
24 Pickup framing
25 Inst plank
23-27 Protection
34 Framing & Plank Elect Closet

58 Men

5-13-70 Cloudy RAIN
Wednesday

5/8 Core - Mater 9 to 16
5/8 Core Planks 10 to 13
41 ft No Activity 8 to 10 AM
Spraying Team 39
Car #5 - When & Who is going to move material from in front of each floor openings

34 - Plumbing Top track & Inst
27 Studs & Framing Elev Beams
25-26-27-28 - Plank shaft 37-38
24-25-26-27-28 Pick up framing
24 Plank & sheet
25 Plank & sheet
25-30 Protection (58)
44-45 Layout

Car 6-7 Rails up to 55

29 floor stair Post West stair
Removed Gold Hats

5-14- Cloudy

Sample Elev Back 16 floor
With Sheet Rock Shafts 28-29
Sample Elect Closet 32 fl
South West - Sheet Rock

113 Spraying Trusses 39
Scraping 41 - 2 men

35 - Plumbing Top Track & Inst Top Track
27 Studs
34 Inst Backs & Framing Stairs
44-45 Layout
45 Tool Cr
24 Inst Plank & Sheet
24-25 Pick up framing
25 Inc Plank & Sheets above 26
~~26~~ 8 Men on Protection
total 58 men -

5-15 - Friday Fair

(113)
Scraping Bott Flanges of Beams 41 fl 2 men
17 Comp NW
12 1/2 Comp SW

(110)
Top Track - 36
Plumb top Track 36
Framing Stairs & Backs 33
Framing Elev Shaft 24-25-26-36
Inst Studs 27
Layout 45-46
Const Ladder 39 fl.
Plank Elect Closet & framing
Plank & Sheet 25-26
Plank Elev Shaft 36 - 24-25-26
Pick up framing 25--26
Inst Plank 27
Protection 8 men
Total 58 -

5-18-70 Monday
Cloudy-Rain

113

5-16 - Sat 2 Men Scraping Bott of Flange on 41 fl - as per Jimmy Blue Eye. All flanges are Scraped except 3 - could not get them - has 2 men cleaning floor near Star Circle - As of Friday 5-15-70 No 4" SR is to be used over joint Boards - Tape should be used - SC has contacted Bert Alumintum for change on this - SC Has not as yet received order to use dashes under Heads of Forms.
Checking on Why ASTR3 Beads do not have release Holes in Stitch joint? -

5-19 - Cloudy
Later Rain

110

26 fl Plank & Sheet & Pick up from
27 Plank & Sheet
29 Plank
38-5 - Layout
39 Loader
27-28-29 Forming Shaft 39-40-41
29 Set Studs
36 Forming Stairs
38 Plumb Top Track & Set Top Tr

113 - Spraying Cope on Trusses 39 floor
Cleaning 41 floor.

Testimony Stu 4 Men to clean floors ahead of Layout - 2 are on 5 - 2 on 38
(inserted above "Men": Follows)

5-20-70 Fair

Color of ornament green - as per Mr Osborne - to be started - Monday 25-70 -

Port 113
110 1/2 Day

Parade today

Gave Mem to
Freccumelli on 32 fl Elect Cl
and Conroe on Dic to shop
for Marble 10 fl
to Do same - to Curr Eq.
& not to spray back flag
on Machine Room

5-21-70 Fair

113
41 fl. East Center Elev
Cars Scraped

Spraying Beams 40

Elevator Bucks Re. Core Wall



x started 2 1/2"
x changed 2 1/4" up to x
x changed 2 1/2"
x changed back 2 1/4" ?

Layout 4-5-39
Form & Planking Closets Elect
Plank & Sheetrock 27-28
Pick up forming 28
Plank Stairs 30
Plumb Top Track 39
Inst top Track 39
Inst Studs 30
Forming Stairs 36   52 men

5-22-70 Friday
Fair

Bid Meeting
Hardware Not Meeting on Subject
4" Sheet Rock - Non Min
2 1/2" Elev Frames - Stay as is -
32 ft Sample

Ornament Color is Blue

Layout Mach Room 17-18-19-4
Layout 39-40
Top Butt Track 35-36-37-38-
Jamming Doors El. 37-38-28-29
Duct Stick 30
Top-Butt Track Mach Room 17-18
Block Shattuck 28-29
Block - 30
Build up Jamming 29
Block - Staff 37-38 - 29-30-31

Shaft J-22 Cont
H35 Temp Pert Comp
42 Car operator Come 8:50
Car Not Working - Otis
Men Working Trying to Start
Floor are not Cleaning.
Rack - Pleasant Elev Bucks
& Hanging Doors 11 floor 24-26
Marble Men Removing & Re
Caulking 10 ft Joints at [illegible]
& Bucks - Bosigen
Frank Haltzman had Don
DePaulo of Otis on Job to
Chop Recess for Marble Don
Stated that he would have
men on Job this Afternoon
Protection in Elev Door & Jams
removed - have Otis Protect
their Work -
Spraying Beam 40 ft 1 Man
1 Man Cleaning
1 Man Chopping Recess
1 ft for Marble Base This
Afternoon

5-25-70 Cloudy Rain

11 : Spraying Blue overcoat 11 floor S W Corner. Color very pale - Di Bona will add more coloring to make darker

Layout 40-4
Planking Top Track -39-40
Forming Stair 38-39
Bolt Track 33
Joint Heads 31
Forming Motor Room 18
Plank & Sheet 29-30-31-32
Pick up forming 30
Joint Plank 31
Protection 29-30-4-5

43 Cpt
2 Lab
2 Apprentices
1 Steward
3 Foreman 1 Ast Supt 1 Supt

(53) Prd.

Marble - None

Vin of Sta
26 Cpts - 1 Foreman

DiBona - 2 Sprayers Overcoat
1 Sprayer Cafe
1 Laborer Cafe

5-27-70 Fair

113 - Blue Overcoat Sealer
5 gal Cafco Bond Seal
15 gals Water
~~2 containers Heat Blue Afflaps~~
~~6 Hol. Reffle Cap~~
200 oz Coloring Chromium Oxide
60 oz Water

→ Mfg by Colorizing Associates
Chicago Ill.
. Mat is Combustible

P Bank Saddles 24 to 38 Ready
for grout Will Start Tomorrow

48 - 35 to 25 Inc Saddle grout

Scuring 9th floor 43
Shaft 2 Drop Plank
above landed in 6

40R-21-22-23 North 38-39 H
45-46 East 45--8-9-10 South

5-27-70

Core Board & Sheet Rock
#5 Shaft South 7-1/2
well 5 # 48 - Core only
from 39 Down

Layout 3-41
Inst Bott Track 35-5
Inst Studs 32
Top Track 6-5
Plank-Sheetrock 29-30-32
Plank Sheet Shaft 5-48 - 36 to 40
Pick up framing 31
Total 57 men

5-26-70 cloudy

Check Distance bet Steel Studs 16"o/c

Protection of Cars # 34 - 42 Cap
Nothing on 35 - 43 - 5

Spraying Capes on 6th floor
Not spraying anymore on 10 fl
ran out of Material

Som - Mock up of Outlet 10 fl.

Van Shaft 16 jump to 6 9 floor (54)
Prior to June 10

Checked with Surveyors - Saddle
running 3/16 of dimension 1 at
3/8
Protection on part of Shaft #5 - Latches
on Doors -

5-26-70

Lesson Tanges Where
DeBrown is Carry[illegible]
40 floor El Back a jump
Temp Protection Shaft 42

Layout 40-41
Top Butt Track 32-33-34-35-36-37-38-39 5-48
Set Plank 32-33-34-35-5-48
Protect 32 to 39 - 5 & 48 - 30
Set Studs 31-32
Butt Track 33
Plumb Top Track - 6
Forming Stairs & Backs 6
Set Plank & Sheet 31-30-29
Pull up forms 30-31 (54)

---

35-43 Test Run [illegible] -
[illegible] 40 K — 5 min / form
[illegible] Com 10:15 PM
8 AM-4:30 PM 4:30 Worked to 3:30 AM

5-28 Fair

Layout 3 third - 41
Plank & Sheet 39 to 41 - 33 - 32
31 30
Bolt track - 36
Studs 33
Joining Elm Backs - 32 -
Top track - 6 - 5

Maint - Loose Wire Doors etc
Sunday Work 7 hour
Car 6 - 7 do All
Shafts -

---

Spraying overcoat 11 H

---

Shaft 7 - Tower B

---

5-29-70 Friday
Fair Clear

Protection 45 floor 2 shafts
Elev. 51-52 - 2 men

75 ft - No Tackles or guy

Butler
Stair chopped - Concrete left on landing of Stair

Utley -

AWR Buck 5th floor
AKR-4th No Steel to Contract

[redacted]

Friday 5-29-70

(110)

Layout 2-7-41-48
Bolt Tack 36-37
Forming Elev. Doors shafts 45-46-47 36-37
Inst Bolt & tip Track 5-6
Forming Stairs 5-6
Inst Studs 35
Blank & Sheet 31 - 33 - 34
Blank 32
Buckups forming 32
Protection 8 men

54 men

Meeting to Utah ~~Thursday~~ Tuesday PM
Elev Con 36

Sunday - 5-31-70
Fair

Retied - Replaced where necessary Wire Protection on car #7 from 60 fl to Lobby
4 Cpt 1 Foreman 1 Steward

Checked All Work accomplished by Ston Creek up to date from 40 fl to 10 fl Jackson

---

Monday 6-1-70 Clear
Fair

60 fl Temple Toilet
All 1/2 Sheet Rock up on N. E. - W. Walls. & 1/2"
W.R. Sheet Rock up on East Wall

---

Layout 2 to 6 Inc
Forming & Sheet. Bottom Temple 10 fl
Inst Studs 17-18 Mach Room
Inst Studs 6 - 32-33-34
Bott & Top Track 5
Hang & Bucks - 5
Bott Track 4-5
Top Track - 4
Blank & Shed 31-32-33-34
Pick up forming 33
Block - Sheet Machine Room 17
55 men

Tuesday - June 2 - 2'-1
Fair

110 down this PM - Car #36
28 to 33

9:30 PM - Hunting Mats

2 Bore Boards With H Test
Top & Bott "J" - West
Yoke fastened @ H test
200 lb then 750 lb
for load test only
Ticcarelli notified Monette
they don't know who else
was invited - (USG)

Layout 2 to 6 Doc
Sheetrock Toilet - 10
Plank & Sheet 17-31-32-33
Pick up forming 33-34
Studs 33-34-35-36
Plank 34-35
Stair-Bucks - 4
Bolt Track top Track 4    55 Men
Operating Staff #36 - 28 to 33 Doc
19 Cpts - 2 foreman
- Bomb Threat -

---

Release 9th floor Shafts

Star to Plank way
5th floor as per J Ticcarelli

113 Dr Brown Zero
Reg as yet have to
Wait for Dr Brown to get bom
fm FLA

Sample for Test set up on
10 floor S.W Corridor

Star Well start Wild Air
on 10 fl to complete all Walls

Started to Install Damper
Units Br [illegible] E.c. [illegible]
SE Elev

Wednesday June 3 - 1928
Fair

Test Panel
200 lb Test
Deflection A 1/4 B 5/16
700 lb Test
Deflection A 1 1/16 B 1 5/32

Distortion 1/8" 1/16"
after load Released

Joist Studs 36 -
Block 35 - 34 -
Block - Heat 33 - 32 - 17
Putting Up forms 34
Toilet 10
Studs - Block 10
Layout 48
Fixing Elect Closet -
Belt Track 38
Fixing Stairs 3
Top Belt Track 3 - 4 - 10
58 men

Fixing - Soap Piping Test

All Drilling to be Calor Jug
or Removed. Dr Bone

Thurs June 4 - 1970

Holtzmueller - Allen Nelson Chop
Stairs remove debris -
Bert Vicente } - occupying dwelling
Debona } - or remove
Bert Vicente Electrical Closets
4" Strips

Layout 48
Temple Toilet - 10 ft
Grt Bucks 10
Grt Plank - Sheet - 10 - 17 - 18 - 32 - 33 - 34 - 35
Grt Studs - 17 - 18 - 36 - 37
Pick up forms 34
Bott Track 38 - 39 - 10
forming Stairs & Bucks . 3 60 men

Shaft #5 Protection 3/30/11 -
5 - 1 Foreman (7)
1 Shop Steward
Signing Sheet for
Start Bonus 6 - 19 - 70

Shaft #5 - Protection -

Proceeding 10 ft to Complete
Core Board of ~~Sheet Rock~~
Also Sheet Rock on
Electrical Closet as Sample
on 32 floor - Is this
Approved? -

Overcoat spray is only
on Capo D' old ??? ...
Advise -
aspe De Bona -

Friday June 5 1970
Cloudy Rain

4 Men Protection on Car #5

Warren - Pete 10th floor
8:30 AM OK

113 - Spraying 43 fl.
New Copy 32 fl top 6th
& fin 36 up

Notified Warren Re finishing
Tracks inside Core - & 4" Strips

Spoke to Fred Cavuoto Re
closing 10 floor - Fred
stated that Guzman &
Wurster were going to take
De Bona bodily out of office
to 10th floor to settle this
Joe Burk ships to Joe Lee
to leave board out & he
said Bill Stiff - I'm not
going to do what Bert Wurster
told me -

Steve Cabbiness 10 floor - on
Bert Wurster orders. Mr Bona
Must Patch Voids - Had
Frank Holtzreiter on floor He
state Mr Bona's foreman will
do nothing until they ~~have~~
receive orders from office

Car #5 overtime Protection
5 Cpt. 1 Foreman

Layout - 47 - 49 - Plank Sheet 34-35-33 / 10-18
Soft Shts 37-6 Butt Track - 39
Top Track - 40
59 Men

Blackie Layout Man Stan
Rich. W/T Holiday after Joh Albany

Monday — 6-8- Lou

113 - DeBova Spraying 10 Floor
Capco Filling Voids - & Spraying
Deckers Overcoat -
Also patching up PT Cells

Layout 49
Mockup Toilet 10
Inst Bucks 10
Batt Track 10
Inst Studs 10-11-12-36-38
Plank Cl. Short 34-35-18-10-11
Patching Forms 36
Inst Plank 36
Forming Stairs & Bucks - 36
Top Track 40

60 men

Start Mine - Motor Room
& Juricate Room Cal
51-52
43-44 Spray Bar Joists

Tuesday June 9 - 1970

Spraying 43 - ~~44~~ Saw

Jitty Lift -

Patching of

Spraying Overcoat

Layout 49
Top Salt Track - 40 - 45 - 12
Steel 5 - 11 - 38
Plank & Sheet - 34 - 35 - 36
total 59 Men

If Pipe does not Permit
2 Layers of Sheet Rock
use 1 layer of W.R.
Then up with Reg S R
and Lam down as far
as we can go with W R

36 - 37 - 38 (9 floor)

11 up $19 24 Men
3:30 to 8:30 ~~2~~ [illegible]
26 total

6-10-70 - Wed.
Fair

Check Shaft #6 - Jump from
54N 69 - Protected ? -

| | N | E | S | W | Doors |
|---|---|---|---|---|---|
| 69 | | | | | |
| 68 | | | | | |
| 67 | | X | | | |
| 66 | | | | | |
| 65 | X | X | X | | |
| 64 | | | | | |
| 63 | | X | X | | |
| 62 | X | X | X | X | |
| 61 | X | X | X | X | |
| 60 | X | X | X | X | |
| 59 | | X | X | X | |
| 58 | X | X | X | X | |
| 57 | X | X | X | X | |
| 56 | X | X | X | X | |
| 55 | X | X | X | X | |

54. Ready to go down
Elevator Buck B ... Set 51
Bank A

Protect NE Elect Closet
High ... cargo
Star 41 up

Cut Down Doors 48 fl
6 & 7 Begin across top

Wall Studs Tees up 9'0 - Short 1'6"
on ... side on Bowl side 2'6"
~~...~~ 3 Metal Studs on ... Side
opposite 6 Reg

one Horz Stud

Door Buck - Must use 1/2" Sheet
Rock in order to ... 3/8 Tab
System 7/8" B.B. to Stud Pad
West Stair 2nd Balcony ... feet
... & Bolts also East
11 fl ... A Bank 2nd Balcony
Sheet Rock Cut Short in Stairwells

6-10 Conti

Layout 49
Pillar & Shutwork 37-36-35=140
Build up forming 36-37
Inst Steel 36-38-5
forming Stairs 39
Top Track 45
Top Track 2½" 13-11
Sheetwork Toilet 11
Elev Lobby- 11 58 men

6-11-70 Sai Thursday

113- Spraying Barjons 44
clean ... floor 43
11 fl spraying around
Colums closed by Star-
10 fl. 1008 - 1007 - 1006 1004
1003 1002 1001
11 fl 501 - 502 - 503 504 505
506 507 - 508 - 1008 1007
1006 1004 1003 1002 1001

6-11-70

11 - Star Steel closing up
now 11 floor -
Safety Hats -
Plank & Sheet Rock 37-36
Picking Jenny 37-38-10-11
Inst Stairs 37-39-5
Inst Beds - 11-12
2½" Track - 11
Framing Stairs 40
Top Track - 46 60 men

Friday 6-12-70

Fair

118- Star closing walls on
10-11- Not cleaning inside
Wood Planks- "C" channels &
other Debris on Beam flanges
Star laying off 17 men today
Star received Special Letter from
Tishman re damage to Toilet
Pipes by Star - USG Joint Company
Star to write letter to Tishman
Re changing Epoxy to ~~[illegible]~~ Joint Company
[illegible] changes to go to slab
now - on 10 FL they are going
to go from top of 9'0 to slab -
Layout - 46-47-48-49 Ceilings
Set/Plank 38
Ceiling framing 38-39
Mark Sheet - 37-36
Set Hard 39
Top Bolt Track - 43-44
Top Track 46
Toilets - 10 Fl
2 1/2" Studs - 12    Total 60 Men

21




Bench Mark 1/2" off bolt (2)
51 ft - Back A - 1st Column

51-52 - Protection of Bolt 52-5
Complete doors - 5 days

Spraying Copes Bar Joint 44
Patch - 12 -
Spray ornament 12
17 ft East ~~bolt of~~ Elev from
sticking through core beam
app. 5'4 above floor - Have
Burnt off.

Star Ceils Shorty Brothers into 15 Fl
Jute - Speaker Wire - Sound Elec
Cut

6-15-70 Monday
Sam

Check All Elev opening Block A
D Zone 1

Pete VAGNINI

Vert Shafts 39
Pipe Track 47
Block C 38
Block C & Shaft 37
Bolt Track 47
Vert Banks 13
Toilet 12

(44)

---

Punch list Keeping ...
Pertaining to Protection

113 Spraying 6th floor level
44 Box Joints
12 Patching & overcoat

6-16-70 Tuesday

Door Bucks Received 118 frames
Ticket # F-08655 900 clip flags
6-15-70 Ticket date -

Layout 50
Top Track 45-47 -
Int Studs 39
Block 39
Block & Sheetrock 38-37-11
Int Bucks 14
Toilets - 12
Elev Lobby 12-13

45 Men

113 Patching 12
Spraying cement 12
Bar Joists 44

Elevator Bucks - Local -
as per George Hughes

404 Mfg
387 on Job
17 to be shipped
to be used - Zone 1 - A B C D } Zone A
Zone 2 - A-56 }
Zone 1 - A Bank 50
Zone 1 B Bank 10

Wednesday 6-17-70

Top Track 48
1st Studs 39
Layout 58
1st Plank 39
Plank & Sheetrock 38-12
Framing Toilet 11 & Planking - (43 men)
Elev Lobby Sheetrock - 13
Protection - (29) + 1 31

113

44-45 Bear[illegible]
6 Fl
11-13 Protection
Spraying 12 overspray

6-18-70 Rain
- Thursday - Fair

Layout 51-50
Inst Studs 4
Inst Block -
Inst Block & Sheet 5-12
Top Track 48
Top Batt Track 5
Elev Lobby - 14
Pick up framing 14 - 2 & 2½" Stud
Inst Bucks toilets 13
Framing Toilet 11
Sheet Rock Core - 2½ & 2" 10
Taping 11-12 toilets 44

Partition - 30

A-AB214
Starting Tile Walls - 10 floor
West Mens Toilet

~~Starting~~ Starting to finish walls
Corridor - Etc -

Taping 12 floor - spackling
Toilets

Started Core & Sheet Rock 5K

DeBona Same as yesterday

Friday June 19 -
Fair

Sample Toilet Tile Womens #2
10 floor -
21 Door Bucks 10 floor
21 " " Even floors
22 " odd floors - Apps -

Layout 51
Top Track 48
Top Batt Track Elev Shaft 5
Int Studs 4-5
Block & Sheetrock 5-13
Sheetrock - Core 2 1/2 Studs 10
framing Toilet 11
Int Bucks 14
framing 2 1/2" Walls 14
Sheetrock Elev Lobby & Stairs 14
1 Taper - 12-14 (46)

Protection ~~30~~ 29

110

& Corner Bead # A-AB 312

PVA - Plastic -
Sealer.

113 - Page 80 - Dumping
units - Par 3 -

Sunday June 21-1970.

Fair

Star Circle - 100 -

6 Men 1 Foreman
1 Shop Steward

Started feed 9:45 for
Car from Otis

4PM

Worked Still
8 to 5:30
Daily

#6

June 22 - Monday
Rain-Cloudy

44 ft Zone 2 - Back
A - M. Elm Beds
also protect from being
removed by ots on cars
51-52? -

Elect Closet - 40 to 18 Inc
18 ft - 3 Closets necessary
Why - Try 9 to 40
N.E. Comp Inc

Materials & Deliveries in
cont Area - 44-45-46 etc
cannot unload Trucks!

2 Men Port Mori
Cleaned floor Used Area
Ready for Inspection

Electric Closets North
Wagon - must be completed
Scaffold - Approved?

Bring Worked on
Need more Blocking -

Layout 51-52
Top Track 49
Int Studs 4
Block & Sheetrock - 5
Sheetrock 2½" - 10
Taper - 13-14
Top-Bott Track 4
Joining Tools - 17

45 Men - Protection 30

June 23 - Tuesday
Fair -

Layout 52
Top Track 49
Top & Butt Track —
Block & Sheetrock 5
Taper 13
Framing Toilets 13-11-12
Elevator Lobby / 16-17
Punch up framing - 6-4
Frist Studs - 3-4 -
Sheetrock Toilets
First Bucks - 15

30 Revd - 15 non Revd - 45 total
Restricts - 27 - 3 non Revd - 30 total

115
6th floor -
15-16 Patching

8AM - 10:30 PM
14 hrs -

3 men
1 form
1 2/Hrs.
(D)
8:30
12:30
4 hrs

Wednesday
6-24-70 Fair

Layout 53
Top Track 50
Joint Steels 3-4
Pick up framing 6-5
Plank & Sheetrock 4-5
Sheetrock Core 2½" - 10
Sheetrock Toilet 10-12-13
Joint Beads 15
Sheetrock Elev Lobby 17-18
47 men Prod 30 Protection

113-
Patching 17-18
Overspray 13
Mark 2- 6

Thursday. June 25 1970
Fow

Layout 53-54
Top Track 50
Top & Bott Track
Just Studs 3
Plank & Sheetrock 5-4
Sheetrock 2 1/2" Studs - 15
Sheetrock Toilets 10-13.
Just Bucks 16
Sheetrock Elev Lobby 18
Pick up forming 6
Sheetrock Core Walls 10
forming Toilets 12
33 Production . 16 Non Production 49
27 Protection 3 overhead 30

Double Studs at elevs - ?
Dimensions on toilet. Line up
Caulk type of Sheetrock ceiling
Straight edge on walls toilets

---

56 floor. Plates. NW - Elev
26 Clips →
55 floor Comp - all clips

45 Bar Joists
6 - one spray
13 one spray
19-20 Patching
} 113

---

53 Bucks. Below grade
All orders

---

June 26 – Sunday
Rain

Check Book – [illegible] – 3 Stair
Damaged Page 70 Par 32

---

Layout 54
[illegible] 58
Blank off Sheetrock 4
Joint Study 4-3
Picking forming 5-6-15
Sheetrock 2 1/2" 10
Forming Toilets 14
Joint Bucks – 16
Sheet Elev Lobby – 18-19

49 Men 30 [illegible]

A-AB-212-H STU
Open Cost Page 94 Line E
Steel Plate – cut air shaft

~~[illegible]~~
Overspray – 6
Patching 71-22

---

Star Circle 3:30 [illegible]
Platform South Exit
#7 Car – on floors 48-49
8AM – 10:30PM 14 hours.

June 29 - Monday
Fair

Tower A - Elev. Temp 61 & 62
Shaft
7th floor 69-74

Lacquer 9-54
Top track 51
Bott track - 45
Dust Stds 4-3
Plank Sheetrock 4
Sheetrock 2½ 11
Plank Sheet 12
Promy Toilets 14
Dust Bucks 16-17
Sheetrock Elev lobby 19

52 Men 30 Rotation

113 - 45 Bar Joints
Stripped - Patching
Complain that some one is
running Window & Cutting Rope
on Tops - He is getting too many
[illegible] -
Mtg
Loading 48 floor - Con Boom

Steer - 3:30 fail
Straps - 36-37-38
19 fail 23 fl Inc.
11 Men -

Tuesday - 6-30-20

Fair

Layout - 9- ~~8~~

Top Track 51

Bott Track 3

Int Studs 6

Plumb Sheetrock - 2-4-5-

Sheetrock 2 1/2" Studs 10

framing Toilets 13

Core Shaft Walls - 13-10

~~52 Men 30 Production~~

Sheetrock Plumb Toilets 14

Pick up Core framing 16

Int Bucks - 17

52 Men - 30 Production

112

Spraying Bar Joist - 45

Patching - -

Overspray - - 13

Wednesday 7-1-70 fair
W D E [illegible] ~~southern~~

Floor- 1 - 2 3
16 out out ✓ or drink
15 out out ✓ Inside
14 out out Inside
13 out out ✓ Inside
12 out out ✓ Inside
11 out out ✓ In
10 ✓ out ✓ out ✓ Inside a/c
9 ✓ out ✓ out ✓ ~~[illegible]~~ a/c

Lugg[illegible] - 7-9
[illegible] Shutock 4-5-6-14
Top [illegible] - 51-52-2-3
Just [illegible] 3-16
Just [illegible] - 17
Just Shutock - 10

total 51 min - [illegible] -
30 min [illegible]

113
Bar[illegible] 45
[illegible] 14 13
3rd floor 6 [illegible]

~~7-30-70~~ 10-16 on floors
AA 38 to 47 -
Soap Dispenser
10 fl outside
11 fl. Inside Stall

Freight #
70 floors - F08738
77 floors F08824
144 - AK-Ad

Thursday - 7-2-70
Rain

Layout 55
Blank & Sheetrock 4-
Inst Studs 9-3-6-3
Inst Bucks
Inst Sheetrock 2½ Studs -10-11-14-15
Top Track 5 2-3-9
Bott Track 3-9
Framing Toilets
Framing Slem Shafts 4-3-[illegible]

50 Men Prod - 30 Protection

Bar Joints 45
Spray - 14
Patching - 25

Friday 7-3-70

Fair

Layout 55
Top Track 52-53-9
Butt Track 9
Blank & Sheetrock 2-3-4
Set Studs 9
Set Bucks
Set Sheetrock 2½ - 11 - 14
Framing Elev Shafts 41
Set Blank - 3

42 men Production
14 men Protection

113 - No Work Today

Monday
July 6 -   Fair

[illegible] 14/11   113

Layout √6
Top Track √3
Top Butt Track 42 - 8 -
[illegible] 8 - 7 - 17
[illegible] 2 - 3 - 15
[illegible] 2½" [illegible] - 11 - 12

47 men - [illegible]
80 men [illegible]

Craft 108 - Cont [illegible] 29/[illegible]
2 men / [illegible]

110 - 6
113 - 1
108 - 1

Elev #7 Jump to 74 - July 10 -
Elev 61-62 - [illegible] on or before July 3
CBark -

July 7- Tuesday
Fair

High Reilly - Core Marble Ready?
Check A Book } Marble Ready?
B Book }
Line up Napkin & Soap Disp
Inc - Re. Folding Core Board

Craft on 294 Label - Cont
Shorty 2 Men 1 Layer

110 6
113 1
108 - 1

Occupancy - 14

| | |
|---|---|
| Layout | 56 |
| Top track | 53 |
| Top Batt Track | 43-7-3 |
| Just Studs | 7-8 |
| Block - Sheetrock | 3-5-9-15- |
| Sheetrock 2½" | 12-14 |
| Just Beads | 18 |
| Taping | 10 |

49 Men Production 3# 19
30 Men Protection

July 8 - Wed Fair

(112)

Layout 57
Top Track 53-54
Studs 3-7
Plank-Sheetrock 3-5-9
Sheetrock 2 1/2" . 12 - 15 - 22 - 24
Taping-Spackling 1.0 - 11
Bucks 18 H.

51 Men Production
30 Men Protection

---

108 Shorty - 2 Men - 1 Supt

---

113 Overspray 14 H

July - 9 - Thurs. Fair

15 Overspray (113)

---

(110)

Layout 57
Top Plate & Track 54
Joist Studs 3-6
Top-Bott Track 7-8
Plank-Sheetrock 3-5-9
Plank 6
Sheetrock 2 1/2" 11
Taping - Spackling 11
Tallies 15-16-12
Bucks 18

52 Men Production
30 Men Protection

---

108
Shorty on 29 4 Level
2 Men - 1 Supr

7-10-70 Friday - Rain

Car # Box KA - Zone 2 -
Operator on Job - 9:20 Am

Layout 57-58
Top Plate & Track 3-4
Sect Studs 7-8
Block & Sheet 9-16
Sheetrock 2½" - 11-12
Framing Toilet 15
Bucks - 18

50 Men Paid
30 Men Protest

110

Shanty - 284 - 2 Men 1 Helper 108

Overspray - 14
Patching -

113

High Rise - Core Marble Ready ?
Check - Bank A } Marble Ready ?
Bank B }
Tie up Napkin & Soap Disp - 10 fl
Stair - Lobby Core Board ?

Short - clips - where
~~#~~ are not Welded
4 Hole -

3rd floor Stair 2 -
Bill Scheller

106.38' =
103.7' =
2.68' =

7-12-70
Sunday Lou
6 Cpt
1 Hept Jumping Carts
1 S.St. 7 to 74 floor
Daily - 7 AM - 5:30 PM -
Sta 8 AM - 5:30 PM
~~||||~~
||||

---

7-13-70 Monday Lou

Protection - 28
Restoration - 49

Layout 58
Top Plate & Track 55 - 7-8
Inst Studs 7-8
Plank & Sheetrock 6
2½" - Sheetrock 11-12-18
Forming Toilets 15
Inst Bucks 18

---

108 Layout checking
[illegible]
John [illegible]

---

113 - Mr Holt

July - 14 - 1970

Tuesday - Fair

Layout 59-
Top Plate & Track 55-56
Bott Track
Plank & Sheetrock 6-8-16
Sheetrock 2 1/2" 11-13-15-16
Framing Toilets 13
Int Brick 19
Top & Bott Track 7-8
Production 16 Man Bed 34 Bed 50 Total
Production 3 Man Bed 25 Bed = 28 Total
Int Studs 7-8-41

Wbg stud Shoes 24" OC

113 - No Work on This Contract

118 - Drilling Holes in Balcony for Bolt Holes for Railing Posts
2 men
1 day

Wednesday July 15 1970
cloudy -

Star Circle -

Layout 2
Top Plate & Track 5 6 - 2
Inst Studs 41 - 42 - 8
Top Belt Track 8
Sheetrock 11
Sheetrock 2½" - 13 - 16 - 19
Plank & Sheetrock 17 - 16 - 8
Inst Plank 7

80 Men
28 Rest

Rotz Eng
Al Cosmos 10th Below 310
Bob Wright 3rd NE Plaza
McGuire 3rd Center Hall
Dave Brown 10th Tower above 310

Brubeck with Craft Shorty Brodie
Hans Stoll Cecil Sams -
Craft 4 Men
4 Jrym

Shaft #5 - Sat -
Shaft #7 Sun -

July 16 Fair
Thurs.

Layout 2
Top Plate & Track 2
Inst Studs 42-43-44-9
Top & Bott Track 9-7-2
Sheetrock 11
Sheetrock 2½-11-13-17-19
Plank & Sheetrock 6-7-8
Inst Plank
Framing Toilets 16
Inst Bucks 1.9
Pend 50
Dust 20

8 fl - West Elev 29-30 A-B Bulk
8 fl West Elev 29-30 Top. Mort
Concrete NG - Butch Plate [illegible]

---

Questions - Shaft 1-2-3-4
3:30 - 9:30
20 1 topn 39 to 44 Jane
Machine Room 3-4 - under const
310 OK Temp door
44 Temp doors

113
Patching no
Overspray 14-15-16
Spray Bar Joists no

---

108 ~~Drilling Balcony~~
Drill & fastening
Install 264 [illegible] -
Observation Platform

---

Frank Turco 14 Hitchfigs - 20 Head
Pete ~~Vaag~~ Vagnini 4 Hitch figs
fell over debris on floor - Peter Turco
to catch & both fell & got at on
4 Sections - (39 floor) Stairs

Fri - 7-17-70

Fair

Protection (30) -

Production 48

---

Layout - 59

Top Plate & Track 2-7-8

Inst Studs 2-7-8

M.P. & Bolt Track - 2-7-8

Sheetrock 11

Sheetrock 2½" 13

Plank & Sheetrock 40-41-42-78

~~Plank~~ I 17 9

framing Toilet 16-17

Inst Bucks 19

framing Elev Shafts - 44-45

254 Spoke to Zeis Nothing
Lawn Shop Protect around
Plant. Engr Office scheduled
to Return Monday. 7-20-70

overtime Set Project Protection Shafts
#5- Concrete #50

113- Tom B- 7½ H.

Patching -

Overspray 16

Banjoes -

---

110 - overtime 3:30 - 9 PM 1 Hr
Shaft 3 & 4 37 to 44 Inc. 12 Gm / 1½ Hrs
Machine Room, Bank A - 17 floor

---

108 -
Jenkins on observation 284
Roch Ste installing Balcony

---

Fri 7-18-70 3 am.
North West Corner - at Crane
69 Planks damaged - 3x12x20

| | |
|---|---|
| 77 | 18 |
| 76 | 3 |
| 75 | 10 |
| 72 | 3 |
| 71 | 23 |
| 69 | 10 |
| | 67 |

Sat 7-18-70
Fair

Rickie & Vreeland
Concrete

---

Were working outside of shaft # 50 - Fred Concrete stop them. They were pumping Concrete about 2 floor & men were working in Basement - Stones were falling down & they complained - were changed over to shaft #5 to complete.

(50) -

Worked on 5 ~~#~~

7 Cpt
1 Supt } - 8 to 3:30

Daily 8-4:30 Shr

Sun 7-19-70

Worked on 6 - 7 - Protection

7 Cpt
1 Supt } - 8 to

7AM - 4:30 Shr

Sie Eng. Called about
11:45 AM 1st Batter
6 - Pumps
10 - 1 Fork & Ladder
71 floor - fire E+ set up Master

7-20-70 Monday

110 Fair

Production 31 men
Reproduction 47
Layout 61
~~Top Bolts & Handl~~
Inst Hinds 2
Top & Bott Track 2
Sheetrock 11
Sheetrock 2½" 19
Plank & Sheetrock 2-7-9-17-18
forming Tacits 13-17
~~Inst Beats~~
forming ~~Elm Shafts~~

---

Broken unit Lobby on 10 fl
Stoles - 5 Boys Screws

---

17 fl: Never alon should be 20" in 16" - Plumber

---

106
4 floors of Terrazzo 11-12-13-14,
Ellis Port Morris - Delivered
Marble for Elm Book A Ready
A Stairs Inst
258 Cutter starting on Mail Chute

---

408 Croft on Balcony Tower A
Drilling for Railing

---

113 - Macie & DiBove P.
~~Patching~~
Mopping 1½
~~Bar Joints~~
1½ 7

Tuesday July 21
Sai

Layout 61-7
~~Top Plate & Track~~
Set Studs - 2
Top & Bott Track 7-8
Sheetrock 9
Sheetrock 2½" 13-18
Closet & Sheetrock 8-2
Forming Toilets 13-17

Men - 45 - Production
31 Protection

108 Craft
Drilling Holes Balcony Tower
for Railings 2 Men 1 Layer /

106 Atlas Port Morris Good ✓

10ff · Mens Room Tile Walls
App 7 day for Walls - for floor
109 5 day for floor = 1 Team

Transition 11 floor Bank A

113 - Working A Tower

Wednesday July 22 –
Fair

Stay Arch 110
Protection – 31 –
Production – 46 –
Shaft #4 Wire bracing on East Elev
Rec Elevator @ 9:30 Am. – Men
Waiting 1 1/2 hours idling.

Layout 7
Top & Bolt Plate 7-2-8
Joist Heads 7-2
~~Sheetrock~~
Sheetrock 2 1/2" 17
Plank & Sheetrock 18-9-8-2
Toilets – 13

---

Craft Art – Drilling Balcony for Rails 2 Men
Drillers

---

Cutter Joist Mail Chute
294 Level to 310 Level.
2 Men

---

Atlas Post Mains 106

Travertine – 11 floor Back
4 Men

---

Toilets – 2 – 1 P/H Mens
Fitting Walls. 109

---

11 B Du Bois
Nothing

Thursday
110 7-23-70 Fair

Protection 31 - 3 Supr. 28 Men
Production 47 18 Mech 29 Men

Layout 1-61
Track & Bolt Track 7-8-3
Sheetrock
Plank & Sheetrock -18-8-2
Sheetrock 2½" 13-14
Framing Toilets 13-14
Insert Studs 7-2
Tape & Spackle 12
Framing 2½" Stud 20
Insert Bucks 20

8
2
3
4

(258)
Cutler Installation of Mail Chutes 310 Lend to 294
2 Men ✓

(108)
Craft Art Drilling Holes
Balcony for Railings ✓
2 Men 1 Supr

Atlas Port Moving 4 Men
(106) Marston on 12 floor ✓
Elev Bank A.

109 Bathroom 18 floor Tile walls 2 Men

De Bona (113)
Nothing

Sam-Pete-Al-John-

7-24-70 Friday
Saw

Layout 61-7-8
~~Top & Bott Track~~
Sheetrock 2
Sheetrock & Block 7-8-20
Sheetrock 2½" 14
~~Forming Toilets~~
Int Studs 8-2
Tape & Spackle 13
Forming 2½" Studs - 20
Int Bucks 20
Top Plate Top Bott Track 4-5-7
Block 18-20

Production 44
Protection 31

(258)
Cutler - Int 294 A
310 Mail Chute
2 men

Craft Art (108)
Drilling Holes Balcony
for Railing
2 men 1 Supt

Atlas Port Morris 106

Tessitore 12 floor A
BANK A - 4 men

Tile Walls - 10 floor
Toilet
109 2 men

Mountain Bone (?) - 113

[illegible] 17

Monday 7-27-70 Cloudy Fair

Layout Tell Comb 40 to 61 men
Tape & Butt Track 6-7-8-7-9
Sheetrock 20
Sheetrock 2½" 14-20
Plank & Sheetrock 2-3
Inst Studs 2-3-7-8
Tape & Spackle 13-14
Lowering 2½" Studs
Inst. Bucks
Inst Plank - 7-18

Products 41 men
Production 31 men

Protection of Comm. of Thunder by Who & Stan Ref 166 - ®

Circuits Loose

---

108 Craft Art
No Hold on this Contract

---

Atlas Port Morris
106 Transitori (4)
13 floor

---

109 Tile Bl
10 floor 2 men
Harnes Foreman

---

113 Main & Dubin -
Bar Joists 46
Overhead 16

---

258- Cutler
Inst Chute 294 level - 310 level
2 men

7-28-70 Tuesday

Fair

Layout 6 2
Top & Bott Track 9-7
Shaftwalls 20-21
Sheetrock 2½"
Plank & Sheetrock - 19 - 4-5-6-2
Inst Studs 7-8
Tape & Spackle 0
Flooring 2½" Studs - 20-18-14
Inst Backs 20-7
Inst Plank 0
Plank 7

Production 42-
Protection 31-

#6 Jamb - to 80 - 8-7-70

108 Craft Art
No Work Today

106 Atlas Port Morris Terminal
13 floor Brook A - A
4 Man

109 Atlas - Tile
16 floor Tailor - ~~Trailer~~ - A
2 Man

113 Main & DeBone
Bar joints - 46
Ongoing. 17

258 Cutler Mail Chute
2 Man 310/290

Protection Frontier

7-28-70 Wed

(110) Stor Sou

Layout 62-63

Top of Bolt Track 9-7-1-9

~~Sheetrock~~

Sheetrock 2½" 14

Plank of Sheetrock 21-2-7

Set Studs 7-8

~~Tape & Spackle~~

Furring 2½" Studs -14

~~Set Bucks~~

~~Set Planks~~

Furring Toilets 18-14

Production 44

Protection 31

---

Circle Arc 3 Men

-115- Bath, 1 Foreman

Hung Ceiling Corridor

Bedroom - Elev Lobby

---

Who to go to for Certificate Welders for Craft Art (Anyone NYC License)




Caulking Case Walls at Shaft - 175

---

108 Craft Art

No Work Today.

---

106 Atlas Travertine

14 4 Men

---

109 Atlas Tile

11 2 Men

---

113 Marco & Da Bona

Bar joists 46

Ornamental - 17

---

258 Castle

2 Men Beet 310/2nd floor

July 30 1970
Thursday - Fair

Layout 1-63
~~Bed Truck~~ 20-9-8
~~Sheetrock~~ - 0
Sheetrock 2½" 15-18
Block & Sheetrock 19-7
Insul Studs 9-7
Framing Toilets 15-18
~~Framing 2"x4" Studs~~ 0
~~Pipe & Sprinkler~~ 0
~~Block~~ 0
~~Int Studs~~ 0
Elev Lobby 21-22

Production 43
Probation 31 74

---

108 Craft Art
Millwork

106 Atlas Port - Travertine
14-15 (4)

109 Atlas Port Tile
11 (2)

113 Marino Dilone
Spraying Bonfoils 46
overspray 17

208 Cutler Mail
310 to 2nd = 3rd 2 men

115 Quick Arc 10 floor
3 . 5/8 Ninf

Friday
7-31-70 Fair

Layout 63
Top of Bolt Track 310-8
~~Sheetrock — 0~~
Sheetrock 2½" - 22
Plank & Sheetrock 7
Inst Studs 7-8-9
Forming Toilets 18-19
Forming 2½" Studs - 15-18-19
Pipe & Sprinkle 14
Plank — 0
Inst Bucks 21
El Lobby 22

43 Prod
31 Post
74-

---

108 Craft Art
Vat

106 Atlas Transition
15 - (4)

109 Atlas Tile
11 fl: (2)

113 Main & Deb
Bar Joints 46
openings 18

258 Cutler
2 to 3rd - (2)

115 Cecil Ace (3)
10 floor Duct in toilet
mens rm low -

Sat Aug 1. 70
[illegible]

4[illegible]

[illegible] [illegible]

Tieing T[illegible] 50 ft. 4[illegible] -
[illegible] [illegible] 40
[illegible] [illegible]
[illegible]6 [illegible]

1 Joseph [illegible] [illegible] [illegible]
[illegible] [illegible] 8 [illegible]
45 Men - Callyer

Drilling for Casting 60S - 59W
Setting [illegible] 56 - 57
Welding Steel [illegible] [illegible] 55
" " " Joints 54
Pick up [illegible] [illegible] 53
Welding [illegible] [illegible] [illegible]

Monday Aug 3-70
Office   Fair

Layout 1-63
Top Batt Track 8-9-310
Sheetrock 2 1/2 15
Closet & Sheetrock 20-7
Jack Studs 21-8-9-1
Framing Toilet 19
Sheetrock Elev Lobby-22-23
forming 2 1/2" Wall 21
Taping-spackling-20

8-3-70

108 Craft   Office

106 Atlas Transtainer (15)
Office

109 Atlas Trailer (21)

113 Main D. Bonn
Barjacks (46)   Office
Ornamental (18)

258 Cutler   Office

115 Circle Ave (10) Mail

Moving Drill Mach #60
Induction RH Side Bucket 41/1

Star Circle 110

Carpet 5th floor B
Top Batt Track - 59
Forming Elev Bricks - 54
Insert Studs - 9
Sheetrock Elev Lobby - 30
Forming 2 1/2 Studs - 23
Bricks ... 23
Sheetrock & Plank - Lobby - 9
Sheetrock & Plank Toilet 2' - 22
Sheetrock Toilets 2 1/2 - 18
Taping Toilets 17
Sheetrock Core halls - 11

Production 30 + 16 men = 46 total
Protection 33

R 17 - Lou Monday

108 Craft 2 Men - 1 Supt
Drilling & Balancing A Tower
South Elev

106 Atlas Transit 21
21 floor

109 Atlas Tile 14

113 Main Electric
No work with Cat

258 Cotton
No work -

Star Cirk 100

Layout 6 ft - B
Top Belt Track 61-59-43
Leff Study 9
Ploy C Sheetwork 9-L-11
Sheet & Block Tables -22-23
Shegbook Tables 2½" 19
Ironing 2½" Heads 23
Out Backs 23
Type Tables 18

48 men -
33 Men Out
81
4 Lond
85

Tuesday - 8-18-70
Fair

108 - Craft Art
Dilly Balcon 2
1
3

106 Atlas - Tiorations (21)

109 Atlas Tile (14)

113 Marie DeBona
2 Men Benjamin 48

208 Auto
McDonald Cooley

110

Layout B-6
Top Bott Track 61
Ext Studs 35
Block & Sheetrock - 34-35-36
Sheet & Block Joints 23-
Sheetrock Toilets 2 1/2" 23-19
Framing 2 1/2 Studs
Ext Bucks 23
Tape & Spackle - 18
[illegible]
Framing Elev Bucks 62-63
Ext Block - 31-32

51 Men Used
33 [illegible]
4 [illegible]
88 -

Wed - 8-19-70
Fair

108 Graff Art
3 Men on Balcony
[illegible] - Railings

106 Atlas - Fireproofing
22 fl

109 Atlas Tile
14 fl Toilets

113 Mario DeBono
Bm Joists 48 floor

288 Custer

110 Stair 3-8 (Layout Comp)

Layout B — ? 7-8
Top Butt Track 62
Inst Studs 34-35
Plank of Sheetrock 32 L - 34-35-36
Inst & Plank Track 23.
Sheetrock Tacket 2½ 20
forming 2½" Studs -0-
Inst Bucks -0-
Tape & Spackle -0-
forming Elev Bucks 46-63
Inst Plank -0-
Load - 68 ft.
6 hr
1 Men
3 Put
8 8

Jan 5 · 41 Dunn OK

Thurs 8-20-70

Fair

108 Craft Art
Layout & Drilling Balcony
Track A North Elev-

106 Atlas Travatine &
23 Stairs!

109 Atlas Tile (1-4 / 1-2)
14-12

113 Marino & DeBona 48
47 1 man

258 Cutler 28 Ken
MHAK Bird Pay

Metpar - Part on
10 floor mod
256

110 - Star Creek

Layout ~~B~~ 6 8
Top-Bott Track 2-44-45
Inst Studs 44-45
Plank & Sheetrock - 36-37
Plank - Sheetrock Pilots - 23
Sheetrock Pilots 2½ - 20
~~Forming 2½ Studs 0~~
~~Inst Bucks 0~~
Tape - Spackle 30-31-32
~~Forming Elev Bucks 0~~
Inst Plank - L - 11 - 12
Stud,
Sheetrock Elev Lobby - 32

Mtg 10-16 re Protection of marble tile started Monday 8-24

(5 | men)

Friday. 8-21-78

Fabi

108 Craft Art
2 men / Layout Ceiling &
Moldings of Side

106 Atlas Terrazzo (23)
Inst Front. 23 fl El. Lobby
Fla

109 Atlas Tile (12)
Inst Wall Tile 15 fl
Inst Floor Tile 12 fl

113 Mauri de Boer (47)
Bar Joists - 47 2 men

258 Cecilia (2?)
Fla Hydraulic Today

256 Metpar - Toilet Part (10)
Fla As Reported. 8-20-78

110

Layout 60-
Top Butt Leads 63-46-47-42-43
Set Studs 46-47
Block & Sheetrock L-37 $\frac{24}{-}$33
~~Block & Sheetrock Toilets 0~~
Sheetrock Toilets 2½ -20
Framing 2½ Studs -21
Set Bucks 23
Tape & Spackle 10-
~~Framing Elev Bucks 0~~
Set Block 38-12
~~Load~~
~~Sheetrock Elev Lobby~~
Sheetrock - 11

52 Men Prod.
33 Protection & Hoist

89-

Mon - 8-24-70
Fair
108 Craft Art
Drilling of Balcony for Rail 2 Men 1 Supt

113 De Bona
Bar Joists 47-59
4 men

110

Tuesday ~~Layout~~
Top-Bett [illegible] 60-5657
[illegible] 5657
[illegible] 38-3334-24
Sheetrock Toilets 2 1/2 20
Forming 2 1/2 [illegible] -24
[illegible] 24
Tape & Spackle 10
[illegible] L-37-12
Sheetrock 12
Forming Toilets 2 1/2" - 24

33 Protection
52 [illegible]
4 [illegible]
89 -

Tues - 8-25-20
[illegible]

108 Craft Art
2 Men 1 [illegible] [illegible]
N-A-[illegible]

113 [illegible] 47-59

No Work [illegible]

Ceiling Started - (Black Iron)
Tenement Area - Mon
8-24-20 - 2 Men

Armorsote Board [illegible]
does not hold Tape [illegible]
Staples through cloth
Tape & Tape on Marble
OK

110
Star Circle

~~Layout~~ 0
Joint Block Lobby - 12
Block & Sheetrock 38
Top Fl Bathrock 66-49-50
Joint Studs 38-39
Sheetrock Elev Lobby 34
Forming Toilets 2 1/2 - 24
Forming 2 1/2 - 24
Bucks Joint 29
Sheetrock Toilets 21
Taping & Spackling 19
Sheetrock 12

52 Men
33 Port
4 Fore

89

Wed - 8-26-70

Fair

108 Craft Set
2 Men 1 Supt Drilling
Balcony Taken A Holes

113 De Bona
Bar Joint 59 2 Men

2:30 Bar

110 -

Layout 66
Inst Plank 12
Plank & Sheetrock 38
Top & Bott Track 39
Inst Studs 39-40
Sheetrock Elev Lobby 35
Framing Toilets 2½ 24-22
Framing 2½ Studs 24-25
Inst Buck 24-25
Sheetrock Toilets - 24-25 - 21
Taping & Spackling 20
Sheetrock 12
Top Track 60
Framing Elev Shafts 41-42

Production 55
Protection 30
Lost - 4
89 -

8-27-70 Thurs Fan
113 Ben Jones
60-47-50
58

108 - Craft
2 Men
1 Super
Drilling & Balcony
N.C Tower A - for Railings

Crick [illegible] 115
2 Men [illegible] men [illegible]
[illegible] &
Tunnel [illegible] 1

Don Buck K Ave
[illegible] 8-26 Tickets
84 - 66 [illegible]

110 Stor Curb

Layout 49
Inst Block 13-12
Block & Sheetrock 6-39
Top & Butt Track 64
Inst Studs 40
Sheetrock Elev Lobby 35
Forming Toilets 2½" 22
Forming 2½" Studs 25
Inst Bucks 25
Sheetrock Toilets 25-21
~~Taping & Spackling~~ 0
Sheetrock 12
Top Track 60
~~Forming Elev Hoists~~ 0

Production 52
Protection 30
Fixed 4
86

Fri - 8-28-70 [illegible]
113- Main & Du Bone
60 - ~~[illegible]~~ - 50
58

108 Craft
2 Men Inst Balcony
Tower A - Drilling ∅ -

115 Curb Ceiling
3 Men Inst Block On
C & Pencil Studs 10 floor
Tenant Area

9-2-70 7P-7L-1Hop (15) 1613
9-3-70 4P-5L 1F (10) 1614

Mat Not Invoiced
for 8-28

Buck Inst
Mat Loaded
Core Board Inst
Sheet Rock Inst
Protection Stairs
Protection
Toilet Rough Bends
~~[illegible]~~

9-9-70

Rough A Elev - 3 Elev.
by November. 4 others to
come

1 - Wire - flashing -
2 - Star Sealing -
3 - Ditomasso Insulation -
4 - Otto - Paint etc

Everyone clean own garbage if
in doubt Tishman to clarify
& get done -

9-8 3L 2 Iron 2 fm 1615
2 m. 1 Tony (14)
3 men

Wed 9-9-70
Rain

See Star Circle 111 on
Master Sheet check Telephone Boards
10-16 Inc

108 Craft Art - Ducting
& Balcony 14 Elev for
Railing - 1 man OK

113 Main & De Bona
Bar joints (52) - 53 - 55 - (56)
(51) 1 man OK
Comp

115 ~~Ste~~ Circle Ceiling OK
No Work today

4-6 - Spray coat Column ~~Covers~~ ~~[illegible]~~
PM on 4 52-53-55-56 4 men.

(1617) 3 laborers -
~~1~~ mechanic -
3 men Hoisting (7) OK

Thurs. 9-10-70
Cloudy - Rain

Star - 110 - See Master List

---

113 Main & DeBona
Bonforts 53-55 -

Thursday - 4-6 -
Working Sat - 9-12 - Sun 9-13 - 113 -

108 Craft Art
1 Man Dully
1 Helper Balcony A

---

115 - Circle Ceiling
Mr Noel Holley

---

53-55 Shafts
Tonight 4[30] - 7[30]
(13)
(1618)
5 Op -
4 Lab -
5 Machine Men
1 Supt -

---

Fri - 9-11-70
Fair

108 Craft Art
Laying out clips for Lobby Panels
332 Elev South 2 Men 1 Helper

---

113 Main de Bona
Bonforts 53-55

---

Setting 40-41-42-43-44-45
53-54-55 → & in Elev Bank A

---

115 Circle Ceiling
Michael Holley

---

118 Star - See List
Men painting Double
Stud at Back & one
App 68' Away

| | Tues 8-4 | Wed 8-5 | Thurs 8-6 | Fri 8-7 | Mon 8-10 | Tues 8-11 | Wed 8-12 | Thurs 8-13 | Fri 8-14 | | |
|---|---|---|---|---|---|---|---|---|---|---|---|
| | Fair | Fair | Fair | Fair | | Office – Covered | | | | | |
| Layout | 64 | 64 | 65 | 65 | 66 | 3 B | X | | | | |
| Top-Bolt Track | 310 | 55-56 L-21 | 56 | 57 | 57 | 58-57 L | 58 | 58-59 | 59 | | |
| Sheetrock 2½ | 15-16 | — | 16 | 16-17 | | | 17-18 | 18 | 18 | | |
| Sheetrock | 7 | — | — | 24 | | L | L-11 | 11-28 | 11 | | |
| Plank-Sheetrock | 8 20 | 8-20 24 | 8 | 8 21 | 8 | L-8 21 | 8-9 | L-8 9-24 | L-8-9 22 | | |
| Joint Studs | 8 310 | 8 310 | 8 L | L | L 8 | 8-7 L | 9 | 9 | 9 | | |
| Tape-Spackle | 20-21 22 | 23-10 15 | 15-23 11 | 15-10 TC-11 | 10 | 10 | 24-25 26 | 16 17 | 17 | | |
| Forming 2½ Studs | 21 | — | — | 22 | 22 20 | 22 | | | | | |
| Forming Toilets | 19 | 19 | 19 | 20 | | 20 | 20-21 | 21 | 21 | | |
| Elev Lobby | 23 | — | 24 | 24 | L 25 | 26-L | 44 27 | 47-48 49-28 | 48-49 58-29 | | |
| Joint Beads | 21 | — | — | L 22 | 23 | 9 22 | | 23 | 24 | | |
| Joint Plank | — | L | L | — | L | | | | | | |
| Sheetrock Toilets | — | 16 | 21 | — | 21 17 | 17 | 22 | | 18 | | |
| Forming Elev Shafts | | | | | | | | | | | |
| Channels Stairs 1-2 | | | | | | | | | | | |
| Forming Stairs | | | | | | | | | | | |
| Sheetrock Plyboards | | | | | | | | | | | |
| Const Stairs Bank A | | | | | | | | | | | |
| Plank & Sheetrock Toilets | | | | | | | | | | | |

~~Took up~~ With E. Bolond 8-19-70 X

#1892

Car # Jumpers 69 to 80
on 8-9-70 6 Cpt }
1 Foreman } 7 hours
1 Steward }

Covered by Fred Steinguard
Tony out of dept & Approval of Work done & Std Hours for Shafts

| Mon 8-31 ✓ | Tues A 9-1 | Wed C 9-2 | Thurs A 9-3 | Fri 9-4 | Tues 9-8 | Wed Rain 9-9 | Thurs Rain 9-10 |
|---|---|---|---|---|---|---|---|
| 67 | 43 | 43 | 44 | 67 | 67 | X | |
| 64-45-41-42 | 64-46 | 65-64-44 25-40-46 | | | 65-19 43-44 | 65 | 65 |
| 22 | | | | | 14 | 23 | |
| 13-12 | 12 | 13-12 | 13 | 10-13-14 | 13-14 | 14-13 | 13-14 |
| 39 | 39-25-26 | 39-40-26 | 39-40-26 | 40-26 | 40-13 27 | 28-41 | 41 |
| 40 | 40 | 40 | 40-41 | 40-41 | 42 | 41 | 42-41-43 |
| 20-21 | 25-34 | X | 11-12 [illegible] | | Elm Lobby | Table Chairs | Table Chairs 16 |
| | 25 | 25 | 25 | | | 24 | |
| 22 | 22 | 23 | 23 | 23 | 23 | 24 | 25 |
| 36 | 37 | | | | | X | |
| | 25 | 25 | 25 | | | X | |
| 13-40 | 40-13 | | 13 | 14-10 | 14 | 14-13-40 | 40 14 |
| 25-21½ 22 | 22 | 22 | 22 | 22 | 23 | 28 | 28-24 |
| | 44 | 44 | 11-12-13 | [illegible] | | 41 | 41-43 |
| 58 men | | | | 10 | 12-13 | X | |
| | | | | | 43 | 41-42 | 41-43 |
| | 55 men | 57 men | 58 men | 56 men | | 15 | 16 |
| | | | | | 62 men | Bonk A | Bonk A |
| | | | | | | 65 | 65 |
| | | | | | | OK | |

| Fri [illegible] Fair 9-11 | Sun Fair 9-13 | | |
|---|---|---|---|
| 65-66 | Star Circle Jumping Car #7 | | |
| 14 | 6 Gp | | |
| 41 | 1 left | | |
| 43-42 | 1 Steward | | |
| Tel Clond | (8) | | |
| 25 | 8AM 4[20] Till | | |
| 14 | 73086 | | |
| 24-25 | | | |
| 43 | # 1797 | | |
| [illegible] | | | |
| 16 | | | |
| Bomica | | | |
| 29 | | | |
| (65) | | | |
| 31 | | | |
| 96 | | | |

Sat - 9-12-70

113 D. Bra Fair

| | | | |
|---|---|---|---|
| Cow Coliseum | 54- | 2M - 1L | 2 |
| | 53- | 2M 1L | 2 |
| Machine Men | 45- | 1M 1L | 2 |
| 2 - 38 | 44 | 1M 1L | |
| 1 - 48 1 | 43 | 1M 1L | J |
| 2 Super | 42 | 1M 1L | |
| (169) (26) | 41 | 1M 1L | |
| | 40 | 1M 1L | |
| 310 [illegible] Bomica - | | 2M 2L | |
| 24 Men 2 Super. | | 8-4 Men 8-4 Labor | |

(113) Sunday 9-13-70 Fair

| | | | |
|---|---|---|---|
| Cow Coliseum | 54 | 1M - | 1L |
| | 53 | 1 | 1 |
| Machine Men | 52 | 1 | 1 |
| 1-48 | 45 | 1 | 1 |
| 2-38 | 44 | 1 | 1 |
| 2 Super | 43 | 0 | 1 |
| | 42 | 1 | 1 |
| | 41 | 1 | 1 |
| 310 Line Bomica - | | 1 | 1 |
| 9 to 4 - 8 - 4 Labor | | 20 Men 2 Super | (22) 16[20] |

Normal Day 9 1/4 ① 13 1/4 ②
Reg Day 1/6 4 hrs ① 9 1/4 hrs ② 13 1/4 hrs ③

8.5%

Eleven

| | Comp Time | | Total | Exp |
|---|---|---|---|---|
| Sat 4-11-70 | | 8 | 8 | 6.05 ✓ |
| Sat 4-25 | | 9 | 17 | 6.05 ✓ |
| Sat 5-9 | | 9 | 26 | 6.05 ✓ |
| Sun 5-10 | | 9 | 35 | 6.05 ✓ |
| Tues 5-26 | 16 | 8 12:10 | 43 | 5.00 |
| Wed 5-27 | 12 | 4 8:30 | 47 | 2.50 ✓ |
| Fri 5-29 | 16-8 | 8 4:30 | 56 | 6.05 ✓ |
| Sun 5-31 | 9 | 9 | 64 | 6.05 ✓ |
| Tues 6-2 | 12 | 4 8:00 | 68 | 2.50 |
| Thurs 6-4 | 15 | 7 11:30 | 75 | 5.00 OK |
| Fri 6-5 | 11 | 3 7:30 | 78 | 2.50 ✓ |
| Tues 6-9 | 12 | 8-2-4 8:30 | 82 | 2.50 OK |
| Sun 6-21 | 9 | 9 | 91 | 6.05 ✓ |
| Tues 6-23 | 14 | 6 10:30 | 97 | 5.00 ✓ |
| Fri 6-26 | 14 | 6 10:30 | 103 (33) | 5.00 ✓ |
| Mon 6-29 | 12 | 4 8:30 | 107 | 2.50 ✓ |
| Fri 7-3 | 16-8 4th July | 8 (33) | 115 80.90 | 6.05 ✓ |
| Sun 7-12 | 7-5:30 10 | 10 | 125 | 8.55 ✓ |
| Thurs 7-16 | 13 | 5 9:30 | 130 | 2.50 ✓ |
| Fri 7-17 | 13 | 5 9:30 | 135 (28) | 2.50 ✓ |
| Sat 7-18 | | 8 | 143 | 6.05 ✓ |
| Sun 7-19 | | 9 | 152 | 6.05 |
| Fri 7-31 | | 1 | 153 106.55 | -0- |

| Date | Hours | Total | Exp |
|---|---|---|---|
| Sat 8-1-162 | 9 112.60 | 162 (19) | 6.05 ✓ |
| Sat 8-8 4:00 7-5:30 | 10 121.15 | 172 | 8.55 |
| Wed 8-12 4:30/5:30 | 1 (21) | 173 | -0- |
| Sat 8-15 7-5:30 | 10 129.70 | 183 | 8.55 ✓ |
| Tues 8-18 | Shoes - Safety | | 10.00 |
| Wed 8-19 | 1 (139.70) | 184 | -0- |
| Wed 9-9 8-6:30 | 2 hrs | 186 | 2.50 |
| Thurs 9-10 8-6:30 | 2 hrs | 188 | 2.50 |
| Sat 9-12 8-4:30 | 8 hrs | (196) | 6.05 |
| Sun 9-13 8-4:30 | 8 hrs | 204 | 6.05 |
| | | | 17.10 |

196
143 Pd 9-10-70
53 Bal
8
61

(156.80)

| | Status 7-31 | Fair Sat 8-1 | Fair Mon 8-3 | Fair Tues 8-4 | Fair Wed 8-5 | Fair Thurs 8-6 | Fair Fri 8-7 |
|---|---|---|---|---|---|---|---|
| Column Covers - Bill | 39 N | | 39 | 40 Pm 39 | 39 40 Pm | 39-40 Pm | 39-40 |
| Alum Liners John | 14-15 37 N | | 31 | 33-34 | 35-34 | 36-35- | 36-37 35 |
| Caulking Mario | 34 S (156) | | 34 12-2 MEN | 34- (23) | 32 35-34 12-2 (137) | 36- | 36-37 |
| Heads Irving | 36 S | | 37 | 38-37 | 37-38 | 39-38 | 38-39 |
| Cleaners | 29 WN 28 ES | | 28-29 | 29 | 30 | 31-30 | 30-31 |
| Glazing Ed | 26 ESW 27 NES | | 27 | 28 | 28-29 | 29-28 | 28-29 |
| Al Cor & Bulkhead Marty | | | | | | | |
| Spandrel-Sill-Vinyl Irving | 29-30 37 WES | | 37 | 38 | 39 | 39 | 39 |
| Corner Steel | 41-56 | | | | 58 | 59 | 59 |
| Drilling Castings | 59-60 | 59-60 | 59-61 | 61-60 | 61 S 62 N | 64 N 62 W | 63-64 |
| Steel Liner - Richie | 52-53 54-55 | 52-53 54-55 | 52-53 54-55 | 57-56 55-54 | 57-56 55 | 58 56 57 Holes | 56-57-58 59 |
| 41 FL - Set Back Wall Harry | | | | | | | |
| North Lobby - Ed Brown | Insert glass frames | | glass [illegible] | glass [illegible] | Insert glass [illegible] | Insert glass [illegible] | glass [illegible] |
| Castings | 65 | 56-57 | 57 | 57 | 58-59 | 61-60 | 61-62 |
| B 7-8 FL Steel | Steel 4 | | | | | | |
| Lobby Layout | | | | | | | |
| Spray Fireproof. Di Bona | 39-40 40 | 40 | 47-49 | 49 47 | 49-47 | 48-50 | 50-48 |
| Patching Fireproof | 39 | 40 | 39 | 40 | 43 | 44 | 44- |
| Brown Coat | 24 SWNE | | 25 | 25 | 25 | 25 | 25 |
| White Coat | 22 | | 23 | 23 | 23 | 23 | 24 |
| Vermiculite Scratch | 39 | | 39 | 40 | 40 | 46 | 46 |
| Brandt Tony (252) | 27 Steel Channel | | 28 | 28 | 29 | 29 | 30 |

No Water stop, 10:45 AM [illegible] 1PM

Hang Hole Plate Approved?

Shop W Hack

24 Col Con Damage 24-25 [illegible] B/C

Hurt 26 H

| Sat 8-8 fair | Mon Fair 8-10-70 | Tues Fair 8-11-70 | Wed Fair 8-12- | Thurs Fair 8-13 | Fri Fair 8-14 | Sat fair 8-15 |
|---|---|---|---|---|---|---|
| | 40 | 40 | 40-43 | 40-43 44 | 43-44 | X |
| | 36-37 | 36-37 | 37-38 | 37- | 37-38 | X |
| | 36 mabo | 37 | 37-38 | 37-38 | 39 | X |
| | 39 | 39-40 | 39-40 | 39 | 39 | X |
| | 35-32 | 33 | 34 | 35 | 36-37 | X |
| | 30 | 30/109 | 30-31 | 32 | 32-33 | 33 |
| | 39-NES | 39 | 40 | 40 | 40 | |
| | 59 | 59 | 60 | 60 | 61 | 67 |
| 64-63 | 65N-63W | 65-66 | 67-66 | 68-67 | 64-68 | 69 |
| 59-58 | 61-Sills 60 [illegible] 59 59 [illegible] | 61-60 | 62S 60N 61 | 60-61-62 | 65S 64S 63S-62S | 65S-64 67S-63N |
| | [illegible] | [illegible] | | | | |
| 64 make 62 set | 64 make 63 [illegible] | 64-63 90 | 67 make 66-65 | 67 66-65 | 69 m-65 67 | 68-67 |
| 43 E-Lab | 53 E-W 57 | 51-53 | 54-53 | 54-52 | 57-55 | Lobby |
| 46 | 47-46 | 47 | 46 47 | 48 | 48 | X |
| Plant 22 | 25 | X | 26 | 26 | 26 | X |
| Lab | 24 | 25 | 25 | 25 | 25 | X |
| 39 | 47 | 48 | 49 | 49 | 52 | X |
| | 31 | 31 | 32 | 33 | 34 | X |
| Check 45 Tailgate | | | | | | |

4 Taps Burned 56
Fan 4 Elev. Back
Welding of Steel [illegible]
Jambs also 55

South - 26 - 9 West [illegible]
10 East

25 N - White Stairs

Plaster Weld on pans
Plates

Jack Sorrell #49 0451
Jerry Levers Alcoa
Larry Ginbro Cupples

Stair

A-AB-204
205

Test/Insp
[illegible]
8-12-70

204 Unit in 8-12-70 - Stop by Hyp
waited for George Hughs for Phone drop
Wire at 310 unit - 1:15 PM -
449 × 450
1/2" + 1/4" -

1st 200# wt.
2nd 600# wt. } 600# total
Threading unit into Column Counter
Washer

② 451 × 452 West Elev

1st - 200#
2nd - 600# +-0 1/8

ft Cable - 80 ft
ft Travel - 20 floors 40' 40
250 ft

Dick Hoffman -
Tom Christensen

47 Bill Borland

1 Bldg 57 East
56 -

March 30-70
April 1
May 2
June 3
July 4
Aug 5
Sept 6

214 - Toilet Plans & Elev 8'0 F.F./F.C.
215 Ceiling Plan Zone 1
218 Ceiling detail
219 Ceiling detail
220 Elev Lobby Typ. & Elev
221 Elev Lobby details 8'0 1/2"
Tenant Ceiling F.F./F.C. 8'7 1/4"

Aug

| S | M | T | W | T | F | S |
|---|---|---|---|---|---|---|
| 26 | 27 | 28 | 29 | 30 | 31 | 1 |
| 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| 9 | 10 | 11 | 12 | 13 | 14 | 15 |
| 16 | 17 | 18 | 19 | 20 | 21 | 22 |
| 23 | 24 | 25 | 26 | 27 | 28 | 29 |
| 30 | 31 | 1 | 2 | 3 | 4 | 5 |
| 6 | 7 | 8 | 9 | 10 | 11 | 12 |
| 13 | 14 | 15 | 16 | 17 | 18 | 19 |
| 20 | 21 | 22 | 23 | 24 | 25 | 26 |
| 27 | 28 | 29 | 30 | 1 | 2 | 3 |
| 4 | 5 | 6 | 7 | 8 | 9 | 10 |
| 11 | 12 | 13 | 14 | 15 | 16 | 17 |
| 18 | 19 | 20 | 21 | 22 | 23 | 24 |
| 25 | 26 | 27 | 28 | 29 | 30 | 31 |

| Floor | 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 | 20 | 21 | 22 | 23 | 24 | 25 | 2 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Layout | | X | X | X | X | X | / | / | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Top Track | | X | X | X | X | X | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Bot Track | | X | X | X | X | X | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Studs | | X | X | X | X | X | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Core | | - | | X | | | | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Sheetrock | | | | | | | | | | X | / | / | / | / | / | / | / | / | / | / | / | / | / | / | / | / |
| Bucks (Stair, Elev, Hor) S E P | | / | / | / | / | / | / | / | / | S E | S / | S / | 9 / | S / | S / | / | / | / | / | / | / | / | / | / | / | / |
| Chasewall | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2½ Studs | | | | | | | | | | | | | | | | | | | | | | | | | | |
| H-D Metal | | | | | | | | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| H-D Core | | | | | | | | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| H-D Sheet Rock R 5/8 | | | | | | | | | | X X | X X | X X | X X | X X | X X | X X | X X | X X | X | X | X | X | X | X | X | |
| H-D Bucks | | | | | | | | | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Protection | | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| Sheet Rock Ceiling | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Doors | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Soffit | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Corner Bead | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Rigid Insul | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Tape | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Hardware | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Bath Fixt | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Sheetrock ½ W. | | | | | | | | | X | X | X | X | X | X | X | X | X | X | X | | | | | | | |
| Sheetrock 5/8 F.R. | | | | | | | | X | X | X | X | X | X | X | X | X | | | | | | | | | | |

| 27 | 28 | 29 | 30 | 31 | 32 | 33 | 34 | 35 | 36 | 37 | 38 | 39 | 40 | 41 | 42 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | \ | X |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | | X |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | | X |
| X | X | X | X | X | X | X | X | X | X | X | | | | | |
| X | X | X | X | X | X | | | | | | | | | | |
| / | / | / | | | | | | | | | | | | | |
| / | / | / | / | / | / | | | | | | | | | | |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | | |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | | |
| X | X | X | X | X | X | X | X | X | X | X | | | | | |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |

| 43 | 44 | 45 | 46 | 47 | 48 | 49 | 50 | 51 | 52 | 53 | 54 | 55 | 56 | 57 | 58 | 59 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |
| | X | X | X | X | X | X | X | X | X | X | | | | | | |
| X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X | X |

| PART HEIGHT UP TO | SIZE OF GYP PLANK | 'J' RUNNER GAUGE | H STUD # 7.5 PCF TYP | CHANNELS 10 PCF 41-42 | 15 PCF 75-76-107-108 |
|---|---|---|---|---|---|
| 11'-0 | 2"X16" | 20 | 24 GREEN | 24 | 18 |
| 11'-6 | 2X16 | 20 | 22 BLUE | 22 | 16 |
| 12'-0 | 2X16 | 20 | 20 RED | 20 | 14 |
| 12'-6 | 2X12 | 20 | 18 YELLOW | 18 | 16 |
| 13'-0 | 2X12 | 20 | 18 | 18 | 14 |
| 13'-6 | 2X12 | 20 | 16 BLACK | 16 | 14 |
| 14'-0 | 2X12 | 20 | 14 | 14 | 17 |
| 14'-6 | 2½X12 | 16 | 18 | 18 | 16 |
| 15'-0 | 2½X12 | 16 | 16 | 16 | 16 |
| 15'-6 | 2½X12 | 16 | 14 | 14 | 14 |
| 16'-0 | 2½X12 | 16 | 14 | 14 | 14 |

Bar Joists / Floor A
N-S-30 - E-W-14

A Jackson EX-2-4330

Badger -
Al Sidenberg Ni-9-6400
Morty

Hest. - FL-9-6985

Ampleat Davis MO-5-0522

Charles Hoffman
Emery Roth Arc

#6 Shaft 7 hours
#7 Shaft 8-9 hours.

ROYAL
669
Made In America
U.S.A.

Baffles Vertical
1-2-3-4-14-24-36-46-56 57 58 59

Westwood Paper →
384 Lafayette St

Robert Grant
9828 BB "N"

Renick Hill
20-4003

Bob Tell




office - 267-7680 x 28/

Atlas Port Morris  Hugh Riley
914-633-6300
597-9500

Craft Art  291-1116
John Schiavo  267-3210

Sheppard Steel - 937-2700

Marin & DeBono - 732-5222

TONY AVOLA - TISHMAN

LEW GUADAGNO

WRITE IT – DONT SAY IT

CIRCLE FLOOR CO., INC.

UNDERSIDE OF

7TH, 9TH, 41ST, 43RD, 75TH, 108TH, 110TH

PLENUM ROOF SLAB ELEV. 242 -

FA 36
12-54

THE PORT OF NEW YORK AUTHORITY

A-59211

10-19 19 70

W. Schleis
To: R. O'Hara

From: PAUL M. CAVANAGH — 30 Church Street Ext. (61) 39

I-3 – Nos for Contracts 113-115

Contract 113

| | |
|---|---|
| Spraying | 42-51 |
| Clean-up | 51-56 |
| Punch-List | 56-87 |

Contract 115

| | |
|---|---|
| Black Iron | 87-88 |
| Ceiling Tile | 125-126 |

- - - - - - - - - - - - - - - - - -

Narrative Card
Floor # + I-J

PA 36
12-54

THE PORT OF NEW YORK AUTHORITY

A-88211

To: SCHLIEF Room No.

From: Call Room No.

Date 7/7/70

Lou

ZACCARDO 10 AM

215 - 699 - 5270

Laminators Inc —

after 8 AM

Tomorrow

MINORU YAMASAKI AND ASSOCIATES
350 WEST BIG BEAVER ROAD TROY, MICHIGAN 48084

Craft Architectural Metals Corp.
120 Fairchild Avenue
Plainview, L.I.,
New York 11803

Attn: Mr. Charles Senzel

FORM 110 5M 7-69

PA 26
12-54

THE PORT OF [redacted]

A-58211

19

To:

From: E. BOLAND — 53 Dey Street Ext. (61) 61

1/8" = .01
1/4" = .02
ETC.

1" = .08
2" = .17
3" = .25
4" = .33
5" = .42
6" = .50
7" = .58
8" = .67
9" = .75
10" = .83
11" = .92
12 = 1.00

.19
.69

PA 86
12-64

THE PORT OF NEW YORK AUTHORITY

A-89211

7/10 1970

To: W. SCHLEIF/R. O'HARA

From: E. BOLAND — 53 Dey Street Ext. (61) 61

LEROY PORTER
OR PHIL GOZ
620 - 7929

CONTR. 108
CALL. 115
FOR LATEST INFO
ON THESE CONTRACTS

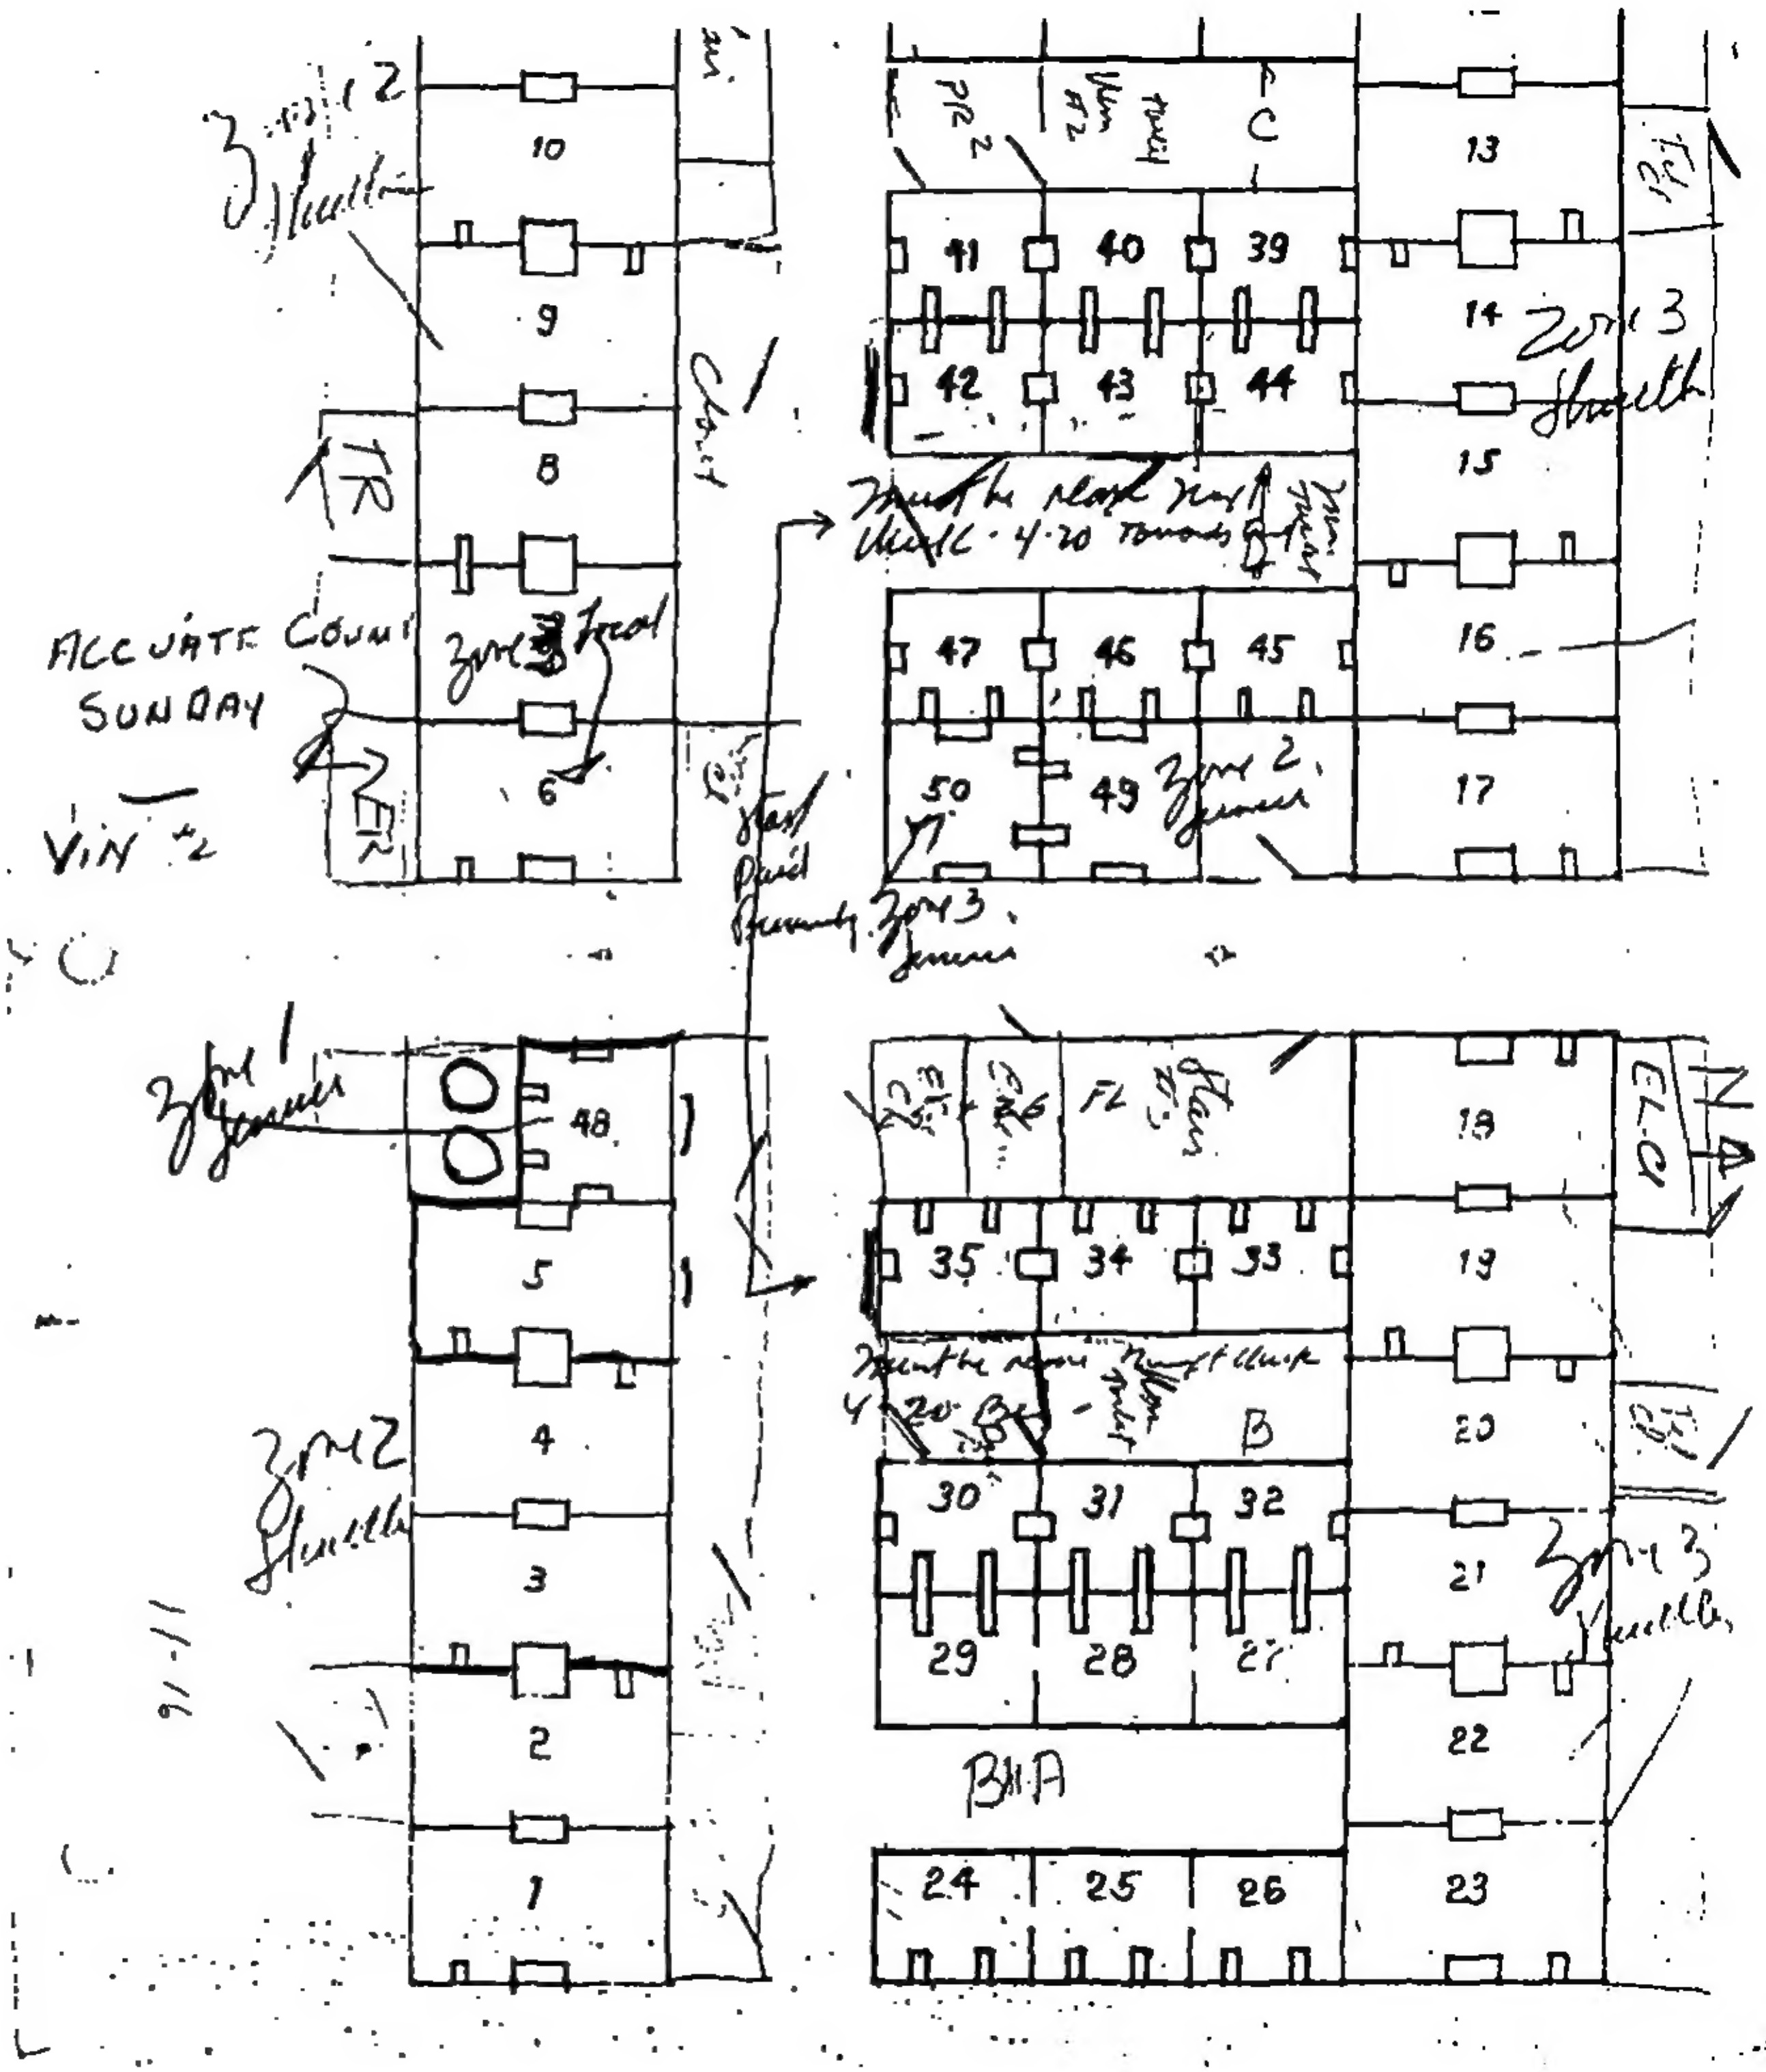

10
9
8
6
41
40
39
42
43
44
13
14
15
16
17
47
46
45
50
49
48
5
4
3
2
1
35
34
33
18
19
20
21
22
23
30
31
32
29
28
27
24
25
26
B
C
TR
FL
ACCUATE COUNT
SUNDAY
VIN #2
Zone 3
Zone 2
Zone 1
Zone 3

# TOWER A ZONE I FLOOR 1

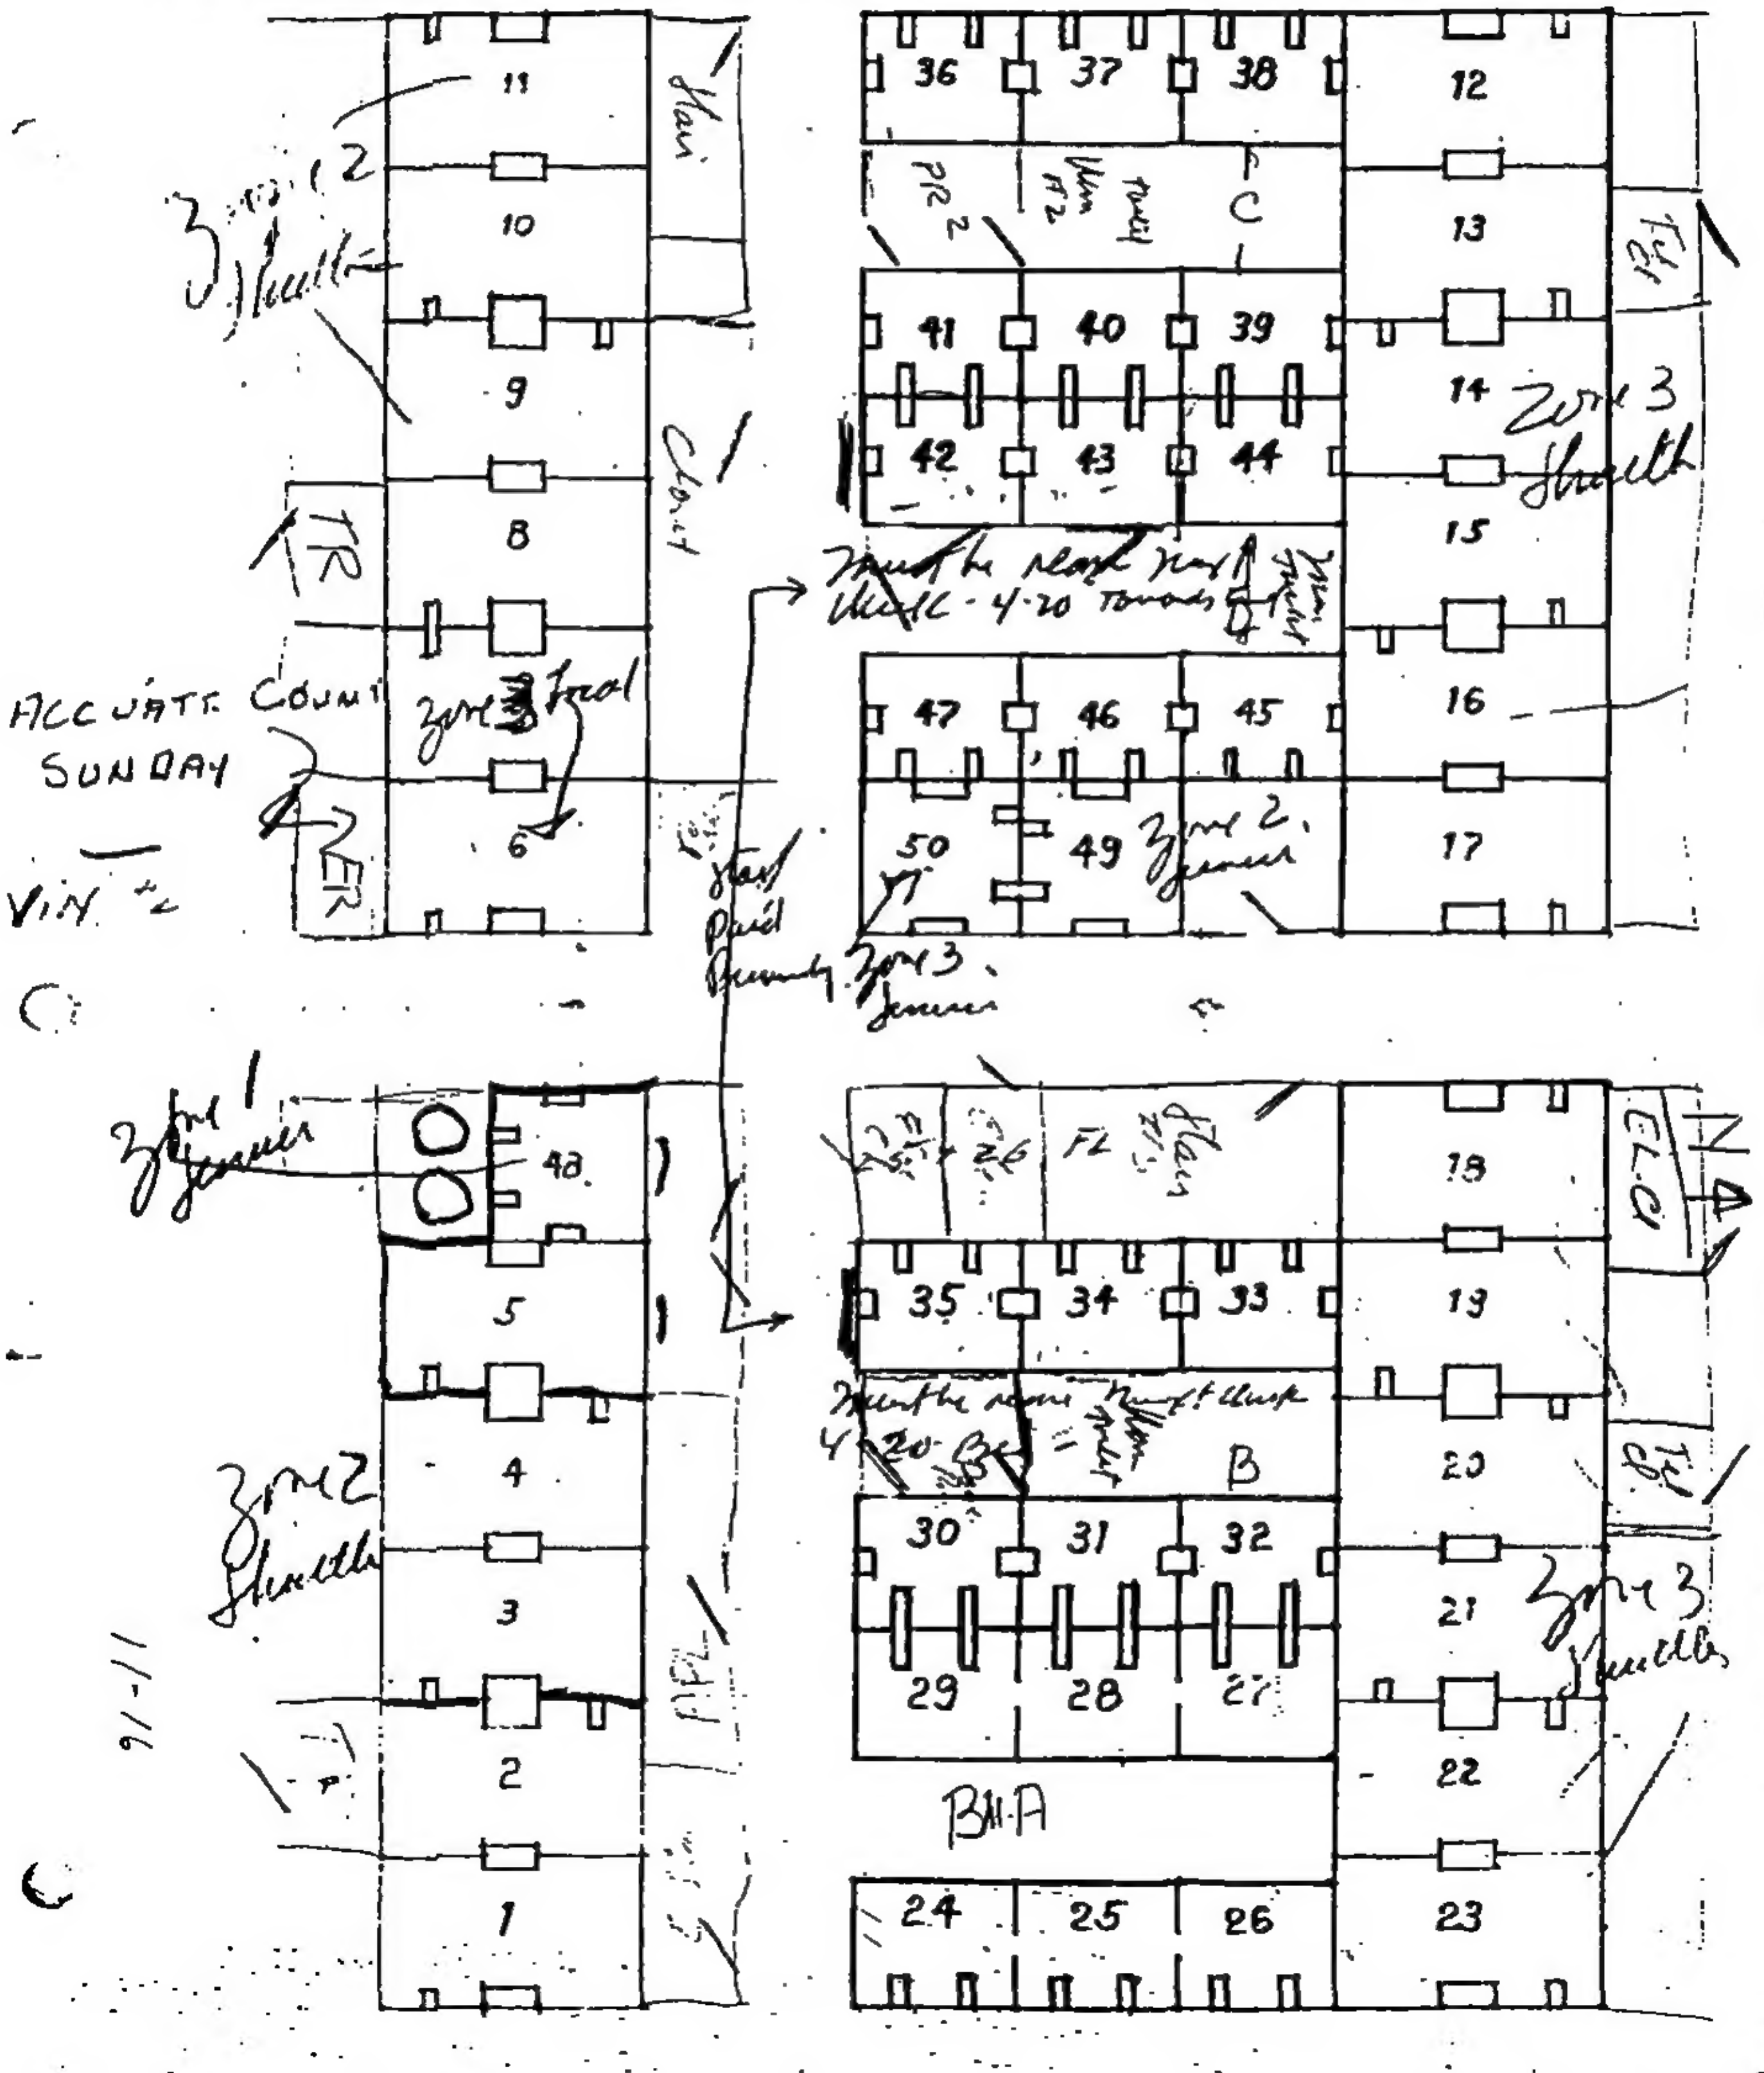

13.07 WORKMANSHIP

1. The Contractor shall completely shield adjacent finished materials including all aluminum or other ornamental metal, cut stone, and all other finished work from splashing by droppings and misdirected sprayed-on fireproofing material being applied under the Contract. Material which may splash against the ornamental metal, cut stone, and other exposed finished work shall be immediately cleansed from the metal, stone or other material with water by the Contractor.

2. Maintaining such adjacent finished materials free from fireproofing material shall be the responsibility of the Contractor. Adjacent and other materials damaged due to improper protection or negligence on the part of the Contractor shall be replaced by him at his own expense.

3. The Contractor shall coordinate with all other trades as may be directly or indirectly involved in the work and shall schedule his work in such manner as to avoid delay in the progress of the work.

4. The sprayed-on fireproofing and sprayed-on insulation, when completed, shall be free from seams, staging breaks, holes, spalls, cracks, flaking and dusting action, and other defects of any kind.

13.08 *CLEANING AND PROTECTION*

1. Upon completion of the application of each coat of spray-on material, on each respective floor, or in each respective area, as may be directed by the Engineer, the Contractor shall remove all debris from floors, walls, and other surfaces, and shall collect and deposit such debris in floor containers which shall be provided by the Authority in each area or on each floor where work is being performed. Debris will be removed by others.

2. During the spray-on operations, floors beneath and around machines, water containers, and mixing boxes shall be protected with waterproofed coverings. All metal and other work adjoining the plastering and spray-on operations, including finished concrete floors, shall be protected and shall be cleansed of all spray-on material and any soiling as may occur, immediately upon completion of the finish coats.

3. Upon completion of the work in any areas, or on any floors, the area or floor shall be scraped and left broom clean. All equipment shall be removed when and as directed by the Engineer.
